City of Richmond

Build Back Better

Project Start Date: 10/14/2021

Scrolling Increment: 10

Milestone description	Category	Assigned to	Progress	Start	Days	End
Affordable Housing						0
Mandatory Workshops	Milestone	Sheryl Hampton	100%	12/2/2021	7	12/9/2021
First Notice of Funding Available (NOFA)	Milestone	Sheryl Hampton	100%	12/10/2021	31	1/10/2022
Rating and Ranking of Applications	Milestone	Sheryl Hampton	100%	2/1/2022	27	2/28/2022
Recommendation of Award and non-Award Notifications Sent	Milestone	Sheryl Hampton	100%	3/24/2022	4	3/28/2022
O&R Adopted for ARPA Budget Reallocation/Amendment	On Track	Sheryl Hampton	100%	3/28/2022	15	4/12/2022
Construction/Rehabilitation Recommendations	On Track	Sheryl Hampton	100%	4/25/2022	30	5/25/2022
Distribution of Grant Awards/Agreements	On Track	Sheryl Hampton	90%	5/1/2022	300	2/25/2023
New Grantee Workshop for next Tranche of Funding availability	On Track	Sheryl Hampton	0%	1/1/2023	120	5/1/2023
Creighton Court						
HCD to draft agreement with the City Attorney's Office	On Track	Sheryl Hampton	100%	3/1/2022	45	4/15/2022

Fe	bru	ary	, <u> </u>														
3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
•																	
F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М

Low risk


On track

Legend:

Med risk

High risk

Final draft agreements to be sent to RRHA	On Track	Sheryl Hampton	100%	4/30/2022	15	5/15/2022
City Department, RRHA, and other related parties meeting	On Track	Sheryl Hampton	Ongoing	5/10/2022	30	Ongoing
Acquire necessary permits	Milestone	Sheryl Hampton	95%	5/1/2022	300	2/25/2023
Abatement/Demo	Milestone	Sheryl Hampton	100%	5/2/2022	151	9/30/2022
Selection of Water/Sewer Contractor	Milestone	Sheryl Hampton	100%	7/1/2022	122	10/31/2022
Infrastructure Work and Completion	Milestone	Sheryl Hampton	0%	9/1/2022	850	12/29/2024
Highland Grove						
HCD to coordinate a meeting between external and internal development team (DPW, DPU, and PDR) to identify roles	On Track	Sheryl Hampton	Ongoing	4/1/2022	30	Ongoing
Feedback on the Preliminary Plat Review	On Track	Sheryl Hampton	100%	2/15/2022	45	4/1/2022
Complete subdivision	Milestone	Sheryl Hampton	90%	4/1/2022	215	11/2/2022
Community Outreach	Milestone	Sheryl Hampton	0%	5/1/2022	400	6/5/2023
Infrastructure Work and Completion	Milestone	Sheryl Hampton	0%	2/1/2023	790	4/1/2025



c

										M	arcl	h																									
21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
																																					F
Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	w	Т



 	 	 	 																														
 	 	 	 ▶	 	 	 	 	 	 	 	 	 																					
 	 											 			 				 								 		 		<u> </u>	 	

City of Richmond

Build Back Healthier

Project Start Date: 10/14/2021

Scrolling Increment: 0

Milestone description	Category	Assigned to	Progress	Start	Days	End
Health Equity Trust Fund						0
Identification of external partner (RCHD) to execute fund	On Track	Maggie Anderson	100%	10/14/2021	180	4/12/2022
Creation of MOU and approval by City Council	On Track	Maggie Anderson	100%	1/1/2022	90	4/1/2022
Execution of MOU	Milestone	Maggie Anderson	100%	3/29/2022	15	4/13/2022
Advisory Committee Formed via RCHD	Goal	Ruth Morrison	100%	4/1/2022	30	5/1/2022
First Plan Submitted to the City (following MOU)	Milestone	Ruth Morrison	100%	5/1/2022	90	7/30/2022
Award Funds (and then cycle continues)	Milestone	Ruth Morrison	50%	6/1/2022	90	8/30/2022

On track Low risk

Legend:

v risk Med risk

ed risk High risl

3	4	ary	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
Ŭ.	Ŧ	,	Ü	,	Ü	,	10		12	13		13	10	1,	10	13	20
1																	
F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М

‹

											Ma	arcł	1																									
2	1	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
																																						H
-	г	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т
	4																																					
	T																																					

City of Richmond

Investing in our Children

Project Start Date: 10/14/2021

Scrolling Increment: 18

Milestone description	Category	Assigned to	Progress	Start	Days	End
Child Care and Parental Supports						
Child Care & Preschool Stabilization and Expansion Grant Solicitation/Awards	On Track	Eva Colen	100%	2/16/2022	90	5/17/2022
Partner Identified/Announced for other \$500,000 Stabilization & Expansion Funds	On Track	Eva Colen	100%	1/10/2022	30	2/9/2022
Partner Identified/Announced for Home Visiting Expansion Grant	On Track	Eva Colen	100%	3/7/2022	30	4/6/2022
Partner Identified/Announced for UPK Cost Modeling Study	On Track	Eva Colen	100%	2/1/2022	90	5/2/2022
Contracts Executed for Stabilization & Expansion Grants, Home Visiting, and UPK Cost Modeling Study	On Track	Eva Colen	100%	4/1/2022	260	12/17/2022
Universal Preschool (UPK) Cost Modeling Study	On Track	Eva Colen	50%	8/1/2022	300	5/28/2023
Universal Preschool (UPK) Revenue Options Memo	On Track	Eva Colen	100%	8/1/2022	90	10/30/2022
Children's Museum Access Grant	On Track	Eva Colen	100%	5/15/2022	120	9/12/2022
RPS Preschool Aftercare	On Track	Eva Colen	80%	8/1/2022	280	5/8/2023
Resources - Diapers	On Track	Eva Colen	25%	12/1/2022	90	3/1/2023
Resources - Sleep/Stroll/Seat	On Track	Eva Colen	25%	12/1/2022	90	3/1/2023

Legend: On track

Low risk

Med risk

risk H


Fel		ary														
3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
▲																
F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S

Maternal and Infant/Toddler Health Landscape Analysis	On Track	Eva Colen	25%	1/1/2023	240	8/29/2023								
Out of School Time Landscape Analysis	On Track	Eva Colen	10%	1/1/2023	240	8/29/2023								
Family Crisis Funding														
Finalize Family Eligibility Criteria	Low Risk	Reggie Gordon	100%	1/15/2022	90	4/15/2022								
Identify Provider Partners who will be qualified to enroll families	On Track	Reggie Gordon	100%	2/14/2022	45	3/31/2022								
Finalize spend plan and timeline	Low Risk	Reggie Gordon	100%	4/3/2022	21	4/24/2022								
Soft launch with first partners and families	Milestone	Reggie Gordon	100%	4/25/2022	14	5/9/2022								
Public launch	Milestone	Reggie Gordon	25%	5/9/2022	280	2/13/2023	▶		> >	 	 			
Parks Master Plan														
Creation and release of RFP	Med Risk	Chris Frelke	85%	1/1/2022	425	3/2/2023								
Firm section	Milestone	Chris Frelke	0%	1/1/2023	180	6/30/2023	 		>	 	 	> >	 	>
Internal planning team established	On Track	Chris Frelke	100%	2/1/2022	45	3/18/2022								
Community Advisory Board feedback	On Track	Chris Frelke	0%	2/1/2023	120	6/1/2023								
Draft Plan Review	Milestone	Chris Frelke	0%	1/1/2024	135	5/15/2024								
Planning Commission and City Council adoption	Goal	Chris Frelke	0%	6/1/2024	210	12/28/2024								
TB Smith														
Release of internal engagement and conceptual planning task order	Milestone	Chris Frelke	100%	1/1/2021	365	1/1/2022								

							_											
Selection of engagement team	Milestone	Chris Frelke	100%	1/1/2022	60	3/2/2022												
Engagement process and conceptual designs complete	Milestone	Chris Frelke	100%	3/5/2022	120	7/3/2022												
Construction documents phase	On Track	Chris Frelke	50%	8/1/2022	270	4/28/2023												
Final UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke	0%	5/1/2023	270	1/26/2024												
All construction complete	Goal	Chris Frelke	0%	1/30/2024	1,060	12/25/2026												
Lucks Field																		
Release of internal engagement and conceptual planning task order	Milestone	Chris Frelke	100%	1/1/2021	365	1/1/2022												
Selection of engagement team	Milestone	Chris Frelke	100%	1/1/2022	60	3/2/2022												
Engagement process and conceptual designs complete	Milestone	Chris Frelke	100%	3/5/2022	120	7/3/2022												
Construction documents phase	On Track	Chris Frelke	50%	8/1/2022	270	4/28/2023												
Final UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke	0%	5/1/2023	270	1/26/2024												
All construction complete	Goal	Chris Frelke	0%	1/30/2024	1,060	12/25/2026												
Calhoun																		
Finalize and execute agreement with RRHA for transfer of Calhoun to PRCF	Milestone	Chris Frelke	75%	1/1/2023	90	4/1/2023	 	▶	 	 	> >	 	 	 		 	 	·
Complete community-engaged design process with residents	Milestone	Chris Frelke	100%	10/1/2022	100	1/9/2023												
Construction document phase	Milestone	Chris Frelke	0%	3/1/2023	270	11/26/2023												
Final UDC, Planning Commission, and City Council approvals	Milestone	Chris Frelke	0%	6/1/2023	210	12/28/2023												


							_											_
All construction complete	Goal	Chris Frelke	0%	1/1/2024	730	12/31/2025												
Southside Community Center																		
Final Design Documents	On Track	Chris Frelke	100%	10/14/2021	290	7/31/2022												
Final UDC and Planning Commission approvals	Milestone	Chris Frelke	100%	7/1/2022	90	9/29/2022												
Final City Council approval	Milestone	Chris Frelke	100%	10/28/2022	96	2/1/2023												
All construction complete	Goal	Chris Frelke	0%	12/1/2023	395	12/30/2024												
James River Branch Trail Purchase and Development																		
CSX negotiations with local and state partners	Milestone	Chris Frelke	100%	2/1/2022	223	9/12/2022												
Land acquisition/lease/or recreational lease agreement	Milestone	Chris Frelke	100%	9/12/2022	142	2/1/2023												
Final design documents, UDC, Planning Commission, permitting and City Council approvals	Milestone	Chris Frelke	0%	12/15/2022	495	4/23/2024				 					 	 		>
All construction complete	Milestone	Chris Frelke	0%	8/1/2024	365	8/1/2025												
Crooked Branch Ravine Bridge																		
Final design documents and UDC, Planning Commission and Council approvals	Milestone	Chris Frelke	0%	5/1/2023	90	7/30/2023												
Public Engagement Process	Milestone	Chris Frelke	0%	2/1/2023	90	5/2/2023	 									 		>
All construction complete	Milestone	Chris Frelke	0%	5/1/2024	675	3/7/2026												
Texas Beach/North Bank Tower Repair																		
Site investigation and CSX negotiations	Milestone	Chris Frelke	0%	1/1/2023	210	7/30/2023	 	 	 					.	 	 		>
																		_


Site selection and design and engineering document creation and CSX	Milestone	Chris Frelke	0%	8/1/2023	240	3/28/2024
Final design documents, UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke	0%	4/1/2024	180	9/28/2024
All construction complete	Milestone	Chris Frelke	0%	10/1/2024	575	4/29/2026
Property Acquisition for new Southside Parks						
Updated land identification criteria	On Track	Chris Frelke	100%	1/1/2022	45	2/15/2022
Solidified land trust and non-profit partnerships	Milestone	Chris Frelke	100%	1/1/2022	45	2/15/2022
Negotiation process established	Milestone	Chris Frelke	25%	5/1/2022	350	4/16/2023
Funding leverage opportunities identified	Milestone	Chris Frelke	0%	12/31/2022	225	8/13/2023
Land acquired	Goal	Chris Frelke	0%	1/1/2023	395	1/31/2024

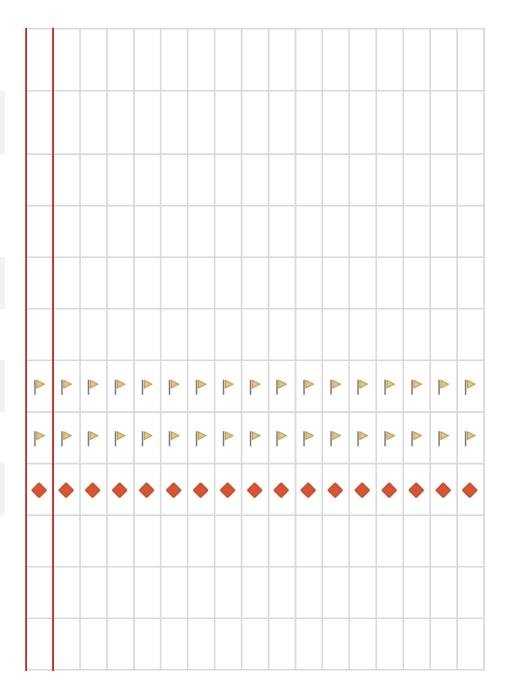

risk

											Ma	arcl	า																									
20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28		
																																					Þ	
М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	T	W	Т

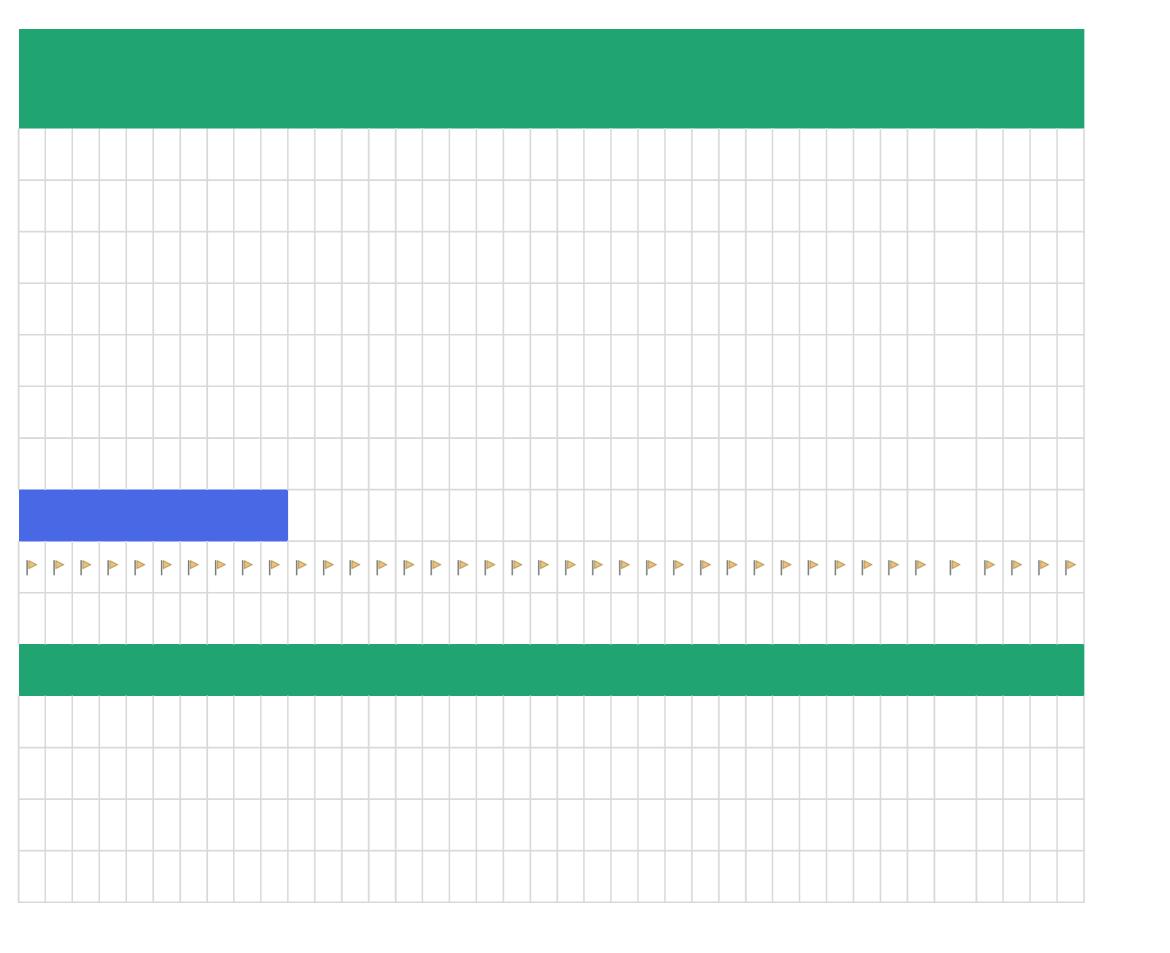

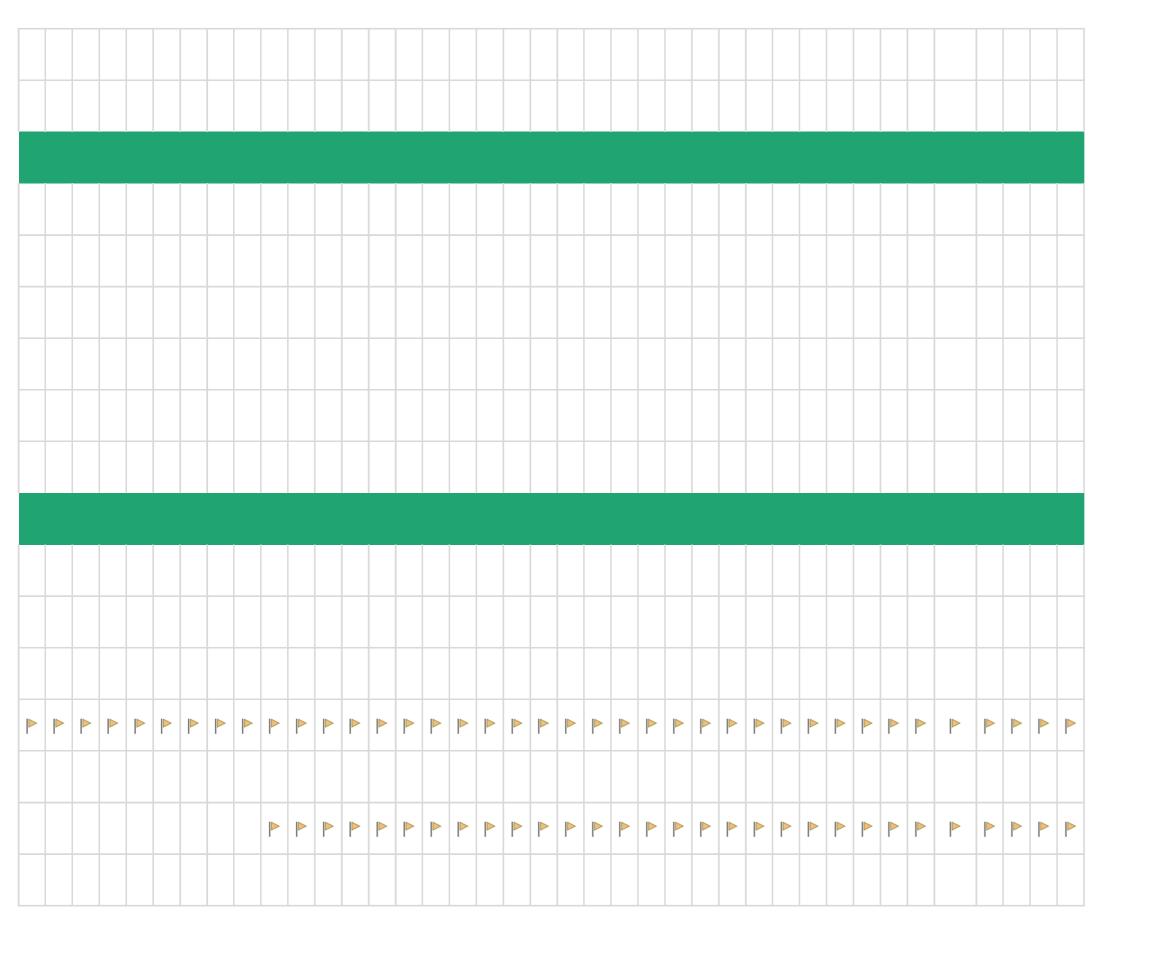



	▶						▶		 																									▶		 		
•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•

City of Richmond

Build Back Stronger

10/14/2021 Project Start Date:

Scrolling Increment: 12


Milestone description	Category	Assigned to	Progress	Start	Days	End
Small Business Grant Application						0
Develop program scope of work	On Track	Pat Foster	100%	1/10/2022	15	1/25/2022
Identified potential partners, service providers and business participants	On Track	Pat Foster	100%	2/1/2022	333	12/31/2022
Select business participants	On Track	Pat Foster	100%	4/15/2022	260	12/31/2022
Start implementation of Triple A program of assessing, developing their respective strategy and	On Track	Pat Foster	100%	5/2/2022	213	12/1/2022
Have at least 5 businesses in the pipeline	Goal	Pat Foster	100%	6/1/2022	30	7/1/2022
Have at least 10 business receive necessary resources	Goal	Pat Foster	0%	7/15/2022	259	3/31/2023
Have at least 20 businesses receive necessary resources	Goal	Pat Foster	0%	7/15/2022	360	7/10/2023
Façade and City Beautification						
Review Design Proposal- consultant to review 20 locations	On Track	Torrence Robinson	100%	1/1/2022	100	4/11/2022
Notice to Proceed w/Design	Milestone	Torrence Robinson	0%	1/30/2023	9	2/8/2023

(On t	rac	k			Low	ris	k		ı	Med	l ris	k		ŀ	High	ri
Fe		ary	/														
3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	2
1																	
F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	N
•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•
•																	
•		•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•


Legend:

Complete Design	Milestone	Torrence Robinson	0%	2/8/2023	90	5/9/2023						
Public Engagement and Outreach	Milestone	Torrence Robinson	0%	5/9/2023	60	7/8/2023						
Construction Start	Milestone	Torrence Robinson	0%	6/17/2023	90	9/15/2023						
Complete Construction and project close out	Milestone	Torrence Robinson	0%	10/15/2023	210	5/12/2024						
OCWB Workforce Development & Community Ambassadors												
Exploring partnerships for Returning Citizen Guaranteed Income Pilot program (age 18+ eligible)	On Track	Caprichia Spellman	100%	4/1/2022	210	10/28/2022						
Launch of Returning Citizen Guaranteed Income Pilot Program	On Track	Caprichia Spellman	50%	6/1/2022	250	2/6/2023						
Planning and design of Workforce Development/skilled trades//Employment Services for 18-24 year olds (Builds off MYA model)	On Track	Caprichia Spellman	75%	3/1/2022	360	2/24/2023						
Mayor Youth Academy Expansion - Applications	On Track	Caprichia Spellman	100%	3/1/2022	30	3/31/2022						
Skills and Trade Development Programs (OCWB Model)	On Track	Caprichia Spellman	50%	8/1/2022	240	3/29/2023						
OCWB Ambassadors	On Track	Reggie Gordon	On-Going	1/1/2022	1,095	12/31/2024						
CDFI Revolving Loan												
Received approval of planned utilization of funds	On Track	Pat Foster	100%	3/21/2022	1	3/22/2022						
Update:Prepare solicitations for service providers. Solicitation will no longer be needed. Grants will be given to qualified CDFI(s).	On Track	Pat Foster	25%	4/1/2022	500	8/14/2023						
Program Asessmetns	On Track	Pat Foster	20%	5/1/2022	500	9/13/2023						

Selection of CDFI(s)	Goal	Pat Foster	25%	11/30/2022	400	1/4/2024
Draft MOU/Contracts	Milestone	Pat Foster	0%	3/1/2024	180	8/28/2024
Implementation of the Program	Milestone	Pat Foster	0%	9/1/2024	790	10/31/2026
OOVID - 19 Administration Reponse Reserve						
Task 1 - TBD		Shelia White/Jason May		1/1/2023		
Task 2 - TBD		Shelia White/Jason May		1/1/2023		
Task 3 - TBD		Shelia White/Jason May		1/1/2023		
Task 4 - TBD		Shelia White/Jason May		1/1/2023		
Task 5 - TBD		Shelia White/Jason May		1/1/2023		

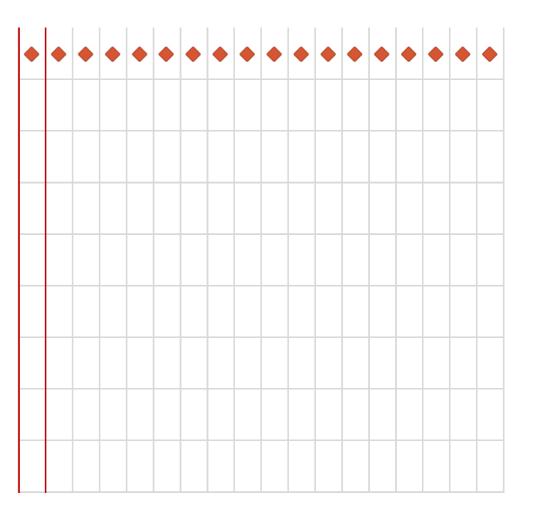

										M	arcl	h																									
21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
																																					•
Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т
•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•
•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•

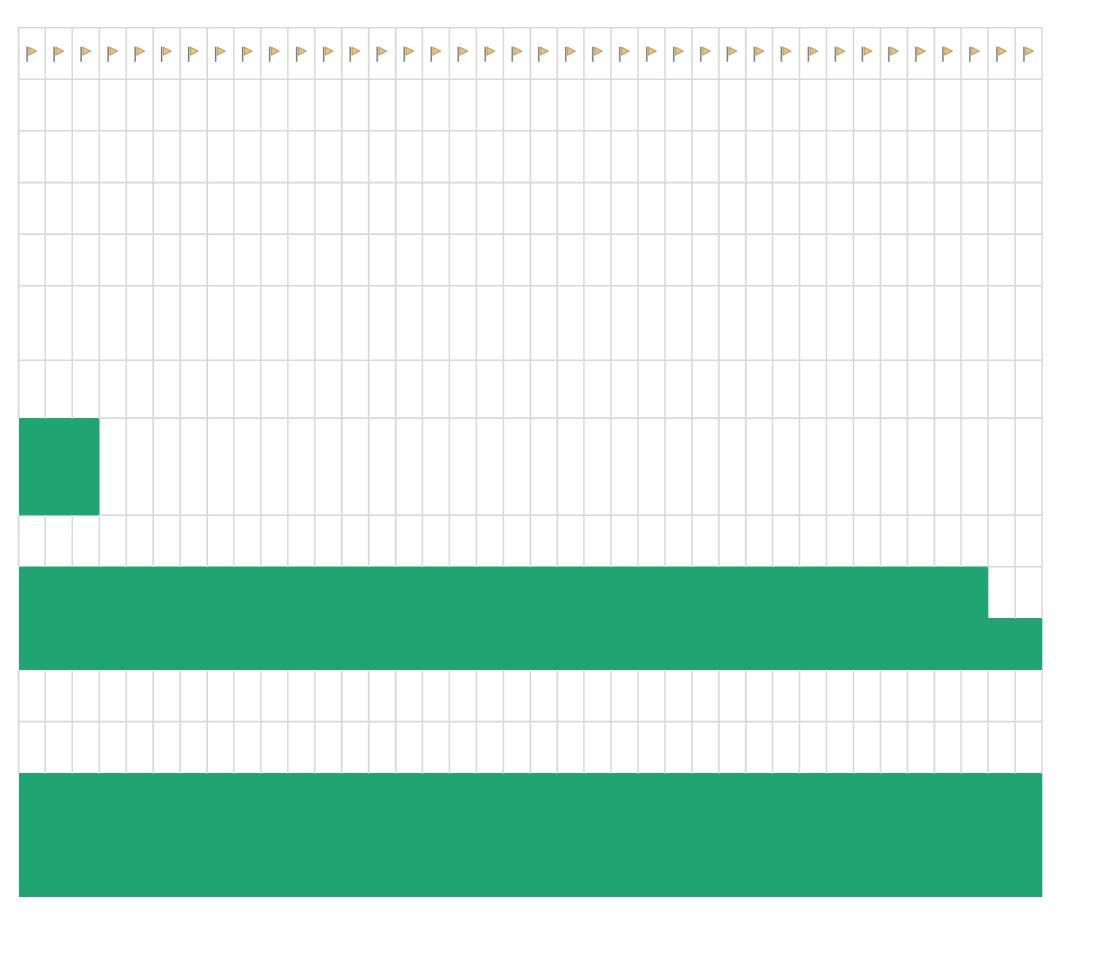

•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•	•

City of Richmond

Building Back Greener and more Resilient

Project Start Date: 10/14/2021

Scrolling Increment: 5

Milestone description	Category	Assigned to	Progress	Start	Days	End
Climate Risk Assessment and Implementation (Project 1)						
Climate Vulnerability & Risk Assessment: Issue RFQ, identify consultant, create P.O.	Milestone	Laura Thomas	100%	1/1/2022	75	3/17/2022
Climate Vulnerability & Risk Assessment: Weekly meetings with consultant to create draft report	On Track	Laura Thomas	100%	3/23/2022	70	6/1/2022
Climate Vulnerability & Risk Assessment: Finalize report for inclusion in RVAgreen 2050: Climate Equity Action Plan 2030	Goal	Laura Thomas	100%	5/31/2022	30	6/30/2022
Urban Forest Master Plan: Draft scopes of work, create and execute work plan	On Track	Laura Thomas	100%	3/1/2022	120	6/29/2022
DPW Hire Urban Forester	On Track	Torrence Robinson	40%	7/1/2022	250	3/8/2023
Urban Forest Master Plan: Establish Project Team	On Track	Laura Thomas	0%	1/1/2023	60	3/2/2023
Solicit RFP for Assessment and select Contractor	Milestone	Laura Thomas	30%	3/1/2023	90	5/30/2023

4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S
		4 5		4 5 6 7	4 5 6 7 8	4 5 6 7 8 9	4 5 6 7 8 9 10	4 5 6 7 8 9 10 11	4 5 6 7 8 9 10 11 12	4 5 6 7 8 9 10 11 12 13	4 5 6 7 8 9 10 11 12 13 14	4 5 6 7 8 9 10 11 12 13 14 15	4 5 6 7 8 9 10 11 12 13 14 15 16	4 5 6 7 8 9 10 11 12 13 14 15 16 17	4 5 6 7 8 9 10 11 12 13 14 15 16 17 18

Low risk

Med risk

On track


Legend:

Develop and Complete Assessment	Milestone	Laura Thomas	0%	6/1/2023	240	1/27/2024							
Solicit RFP for Implementation and select Contractor	Milestone	Laura Thomas	0%	2/1/2024	90	5/1/2024							
Conduct Engagement and Create Plan	Milestone	Laura Thomas	0%	5/1/2024	240	12/27/2024							
Final Plan Review	Milestone	Laura Thomas	0%	1/1/2025	90	4/1/2025							
Planing Commission and City Council adoption	Milestone	Laura Thomas	0%	4/1/2025	90	6/30/2025							
Plant Trees and Project Close out	Goal	Laura Thomas	0%	6/30/2025	180	12/27/2025							
Climate Risk Assessment and Implementation (Project 2 - Citywide Air Quality Monitoring)													
Develop Project Management Plan	Goal	Laura Thomas	0%	2/1/2023	90	5/2/2023	•	•	•	•	•	•	•
Conduct Community Outreach	Goal	Laura Thomas	0%	5/2/2023	120	8/30/2023							
Install Monitors and Record Data	Goal	Laura Thomas	0%	9/1/2023	360	8/26/2024							
Develop Report	Milestone	Laura Thomas	0%	12/1/2023	90	2/29/2024							
Implement Neighborhood Solutions	Milestone	Laura Thomas	0%	3/1/2024	210	9/27/2024							
Project Close Out	Milestone	Laura Thomas	0%	10/1/2024	90	12/30/2024							
Climate Risk Assessment and Implementation (Project 3 - Neighborhood Resilience Project implemenation)													
Develop Project Management Plan	Goal	Laura Thomas	0%	4/1/2023	120	7/30/2023							
Conduct Neighborhood Level Convening Sessions (Round 1)	Goal	Laura Thomas	0%	8/1/2023	360	7/26/2024							

Conduct Neighborhood Level Convening Sessions (Round 2)	Goal	Laura Thomas	0%	8/1/2024	360	7/27/2025						
Conduct Neighborhood Level Convening Sessions (Round 3)	Goal	Laura Thomas	0%	8/1/2025	360	7/27/2026						
Project Close Out	Milestone	Laura Thomas	0%	8/1/2026	90	10/30/2026						
Lead Line Replacement Public Utilities												
Conduct LSL Replacements (on- going)	On Track	Jonathan Cosby	On-Going	6/15/2022	1,650	12/21/2026						
Apply for additional Grants	Low Risk	Jonathan Cosby	0%	1/4/2023	100	4/14/2023						
Develop LSL Inventory Methodology	On Track	Jonathan Cosby	20%	1/1/2022	600	8/24/2023						
BlueConduit Donation of Data Services - Interactive Map	Low Risk	Jonathan Cosby	20%	6/1/2022	300	3/28/2023						
Conduct Inventory	On Track	Jonathan Cosby	10%	3/18/2022	750	4/6/2024						
Develop LSL Public Outreach and Education Programs	Milestone	Jonathan Cosby	10%	3/18/2022	750	4/6/2024					> 	
Submit LSL Replacement Plan to VDH (as required by Lead & Copper Rule Revision)	Milestone	Jonathan Cosby	20%	1/1/2022	985	9/12/2024						
Stormwater - Whitehead Road												
Design	On Track	Bill Boston	100%	7/1/2020	730	7/1/2022						
Permitting	Milestone	Bill Boston	100%	7/1/2022	180	12/28/2022						
Property/ROW Acquisition	Med Risk	Bill Boston	100%	5/1/2021	380	5/16/2022						
Utility Relocations	Med Risk	Bill Boston	50%	12/12/2022	180	6/10/2023						
Contract Award	Milestone	Bill Boston	0%	12/2/2022	90	3/2/2023						


Construction	Goal	Public Utilities	0%	6/10/2023	365	6/9/2024		
Stormwater - McGuire - Phase 2								
Design	On Track	Bill Boston	75%	3/1/2022	365	3/1/2023		
Permitting	Milestone	Bill Boston	0%	2/1/2022	120	6/1/2022		
Property/ROW Acquisition	Med Risk	Bill Boston	0%	2/1/2022	120	6/1/2022		
Utility Relocations	Med Risk	Bill Boston	0%	2/1/2022	120	6/1/2022		
Contract Award	Milestone	Bill Boston	0%	5/1/2023	90	7/30/2023		
Construction	Goal	Public Utilities	0%	8/1/2023	365	7/31/2024		
Stormwater - Broad Rock Manor								
Design	On Track	Bill Boston	100%	1/1/2022	365	1/1/2023		
Permitting	Milestone	Bill Boston	100%	9/1/2022	120	12/30/2022		
Property/ROW Acquisition	Med Risk	Bill Boston	100%	9/1/2022	120	12/30/2022		
Contract Award	Milestone	Bill Boston	0%	1/31/2023	90	5/1/2023		
Construction	Goal	Public Utilities	0%	6/1/2023	365	5/31/2024		
Healthy Homes (Weatherization, Home Rehabilitation)								
Acquire a Construction Specialist/Rehab Inspector	On Track	Sherrill Hampton	100%	3/1/2022	120	6/29/2022		
Secure an Intake Specialist	On Track	Sherrill Hampton	100%	3/1/2022	120	6/29/2022		


Develop Program SOPs/Marketing Materials/General Housing Rehabilitation Specifications	On Track	Sherrill Hampton	90%	5/1/2022	330	3/27/2023
Hold Interest Meetings for Community Outreach	Milestone	Sherrill Hampton	35%	7/1/2022	300	4/27/2023
Receiving applications, ratings, and rankings for selction	Milestone	Sherrill Hampton	40%	8/15/2022	300	6/11/2023



risk

											Ma	arcl	า																									
20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
																																						Þ
M	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т
										 		 						 			 	 					 	 				 		 	 			
									1	1	1	1	1		1		1	1	I	1	I	1		1	1	1	ı	ı	1	1	<u> </u>	1	I	1	I	ı	1	1

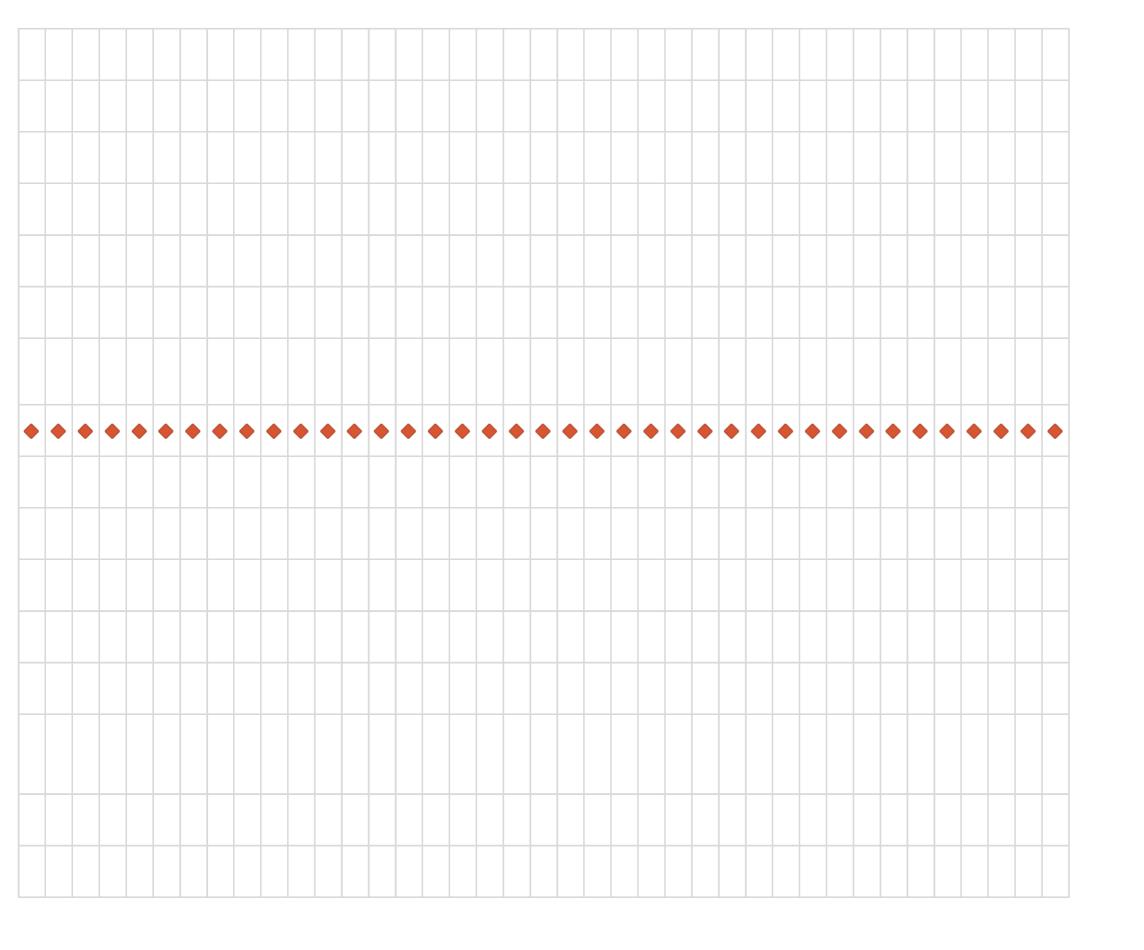

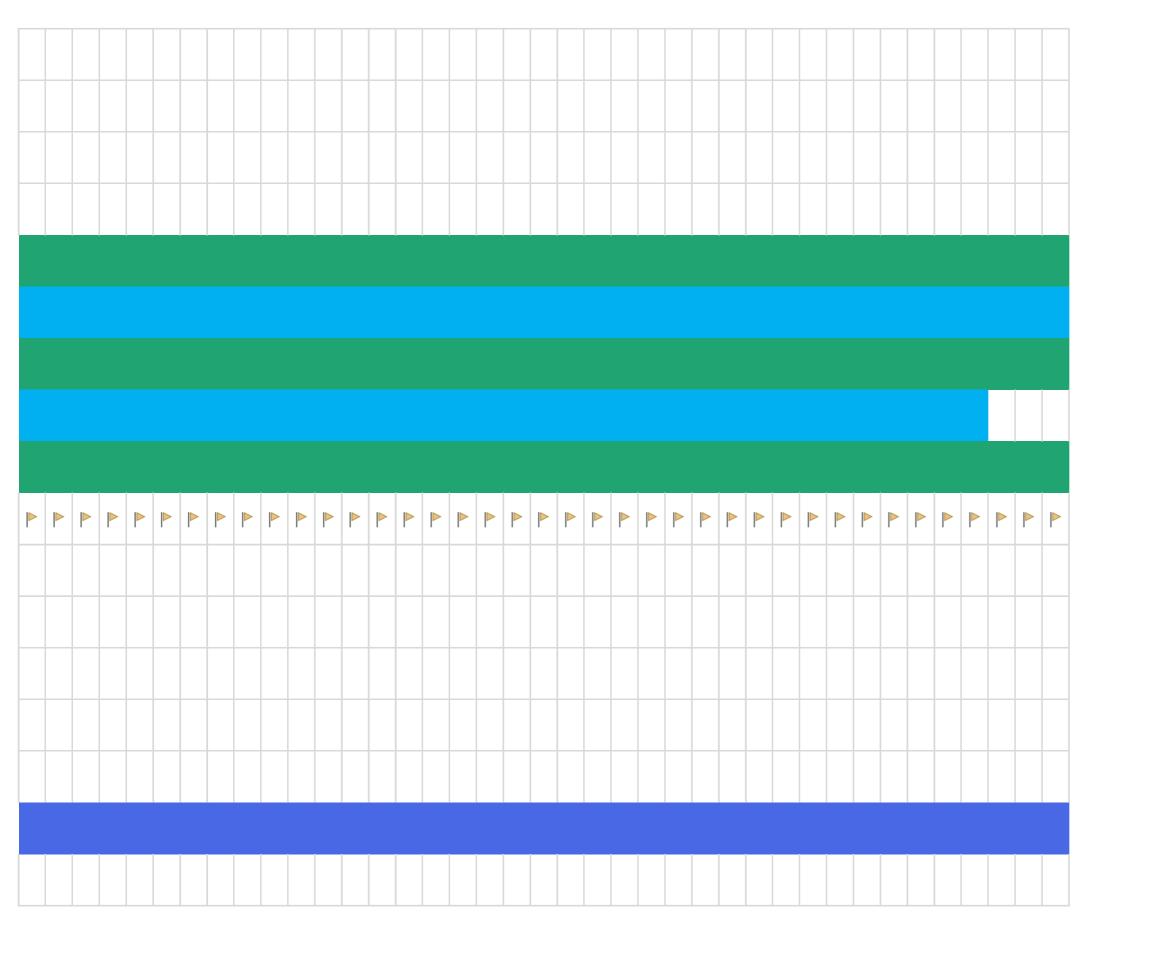



▶	 	 					▶		 	 	▶				▶	 			▶	▶	▶						▶		▶	 		 	 	 	
 			▶	 	 	▶	 	▶	 	 	 	▶	 	▶	 		▶	▶	 	 	 	▶	▶	▶	▶	▶	▶	▶	 	 	▶	▶		 	

City of Richmond


Building Back Safer

Project Start Date: 10/14/2021


Scrolling Increment: 96

Milestone description	Category	Assigned to	Progress	Start	Days	End
Gun violence prevention						0
Identification/Announcement of Positive Youth Development/Youth Violence	Milestone	Eva Colen	100%	1/1/2022	30	1/31/2022
MOU Executed with Fund Partner	Milestone	Eva Colen	100%	2/1/2022	90	5/2/2022
Summer Programming RFP is Posted	Goal	Eva Colen	100%	4/30/2022	1	5/1/2022
Summer Programming Begins	Goal	Eva Colen	100%	6/27/2022	1	6/28/2022
Academic Year Programming RFP is posted	Goal	Eva Colen	100%	8/1/2022	1	8/2/2022
Academic Year Programming Begins	Goal	Eva Colen	100%	9/6/2022	1	9/7/2022
Scope and timeline of Gun Buyback program identified working with RPD and Community	Milestone	Maggie Anderson/ Aaliyah McLean/Megan Field	100%	2/1/2022	60	4/2/2022
Exploring potential third-party partners related to the Gun Buyback Program	On Track	Maggie Anderson/ Aaliyah McLean/Megan Field	100%	3/24/2022	60	5/23/2022
Gun Buyback Program Launch (first Gun Buy Back event)	Milestone	Maggie Anderson/Aaliyah McLean/Megan Field/Spence Cochran	100%	8/20/2022	1	8/21/2022
Planning for second Gun Buyback event	Goal	Maggie Anderson/Megan Field/Spence Cochran	30%	8/24/2022	260	5/11/2023
Second Gun Buy Back event	Milestone	Maggie Anderson/Megan Field/Spence Cochran	0%	4/15/2023	76	6/30/2023

Legend:



First responders hazard pay						
Phase I - Public Safety Bonus for Public Safety	Milestone	Jason May/ Meghan Brown	100%	12/13/2021	10	12/23/2021
Phase II - Public Safety Bonuses for RAA	Milestone	Jason May/ Meghan Brown	100%	3/28/2022	30	4/27/2022
Enhanced Lighting (street and business) and cameras						
Request for quotes and project proposal	Goal	Jackie Crotts	100%	3/15/2022	60	5/14/2022
IT Purchase Request	Goal	Jackie Crotts	100%	4/1/2022	45	5/16/2022
Consultant Procurement for Deployment	On Track	Erich Bessey	100%	4/28/2022	60	6/27/2022
Consultant: Determine CCTV recommendations	On Track	Daniel Dean	50%	2/10/2022	384	3/1/2023
Consultant: Determine lighting recommendations	On Track	Daniel Dean	25%	2/10/2022	384	3/1/2023

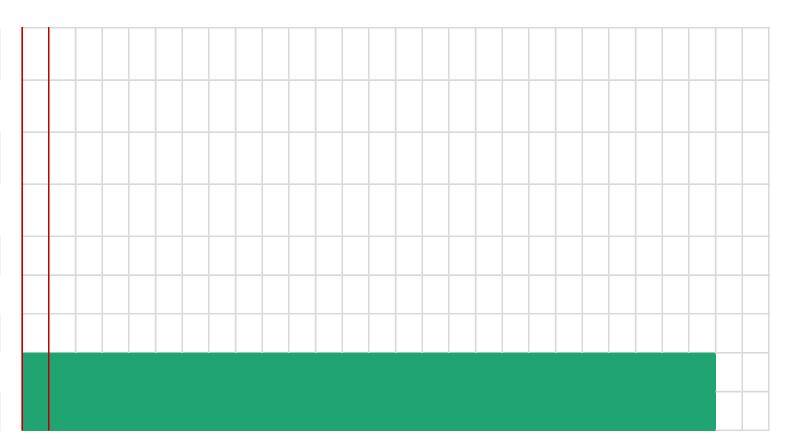

Ma	arcl	า																									
3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	
F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	T
		J		•			'			101				'							•	J	J			•••	

