

ARPA Spending Plan By Priority Area

CATEGORY

Building Back Affordable and Healthy Homes

Affordable Housing Trust Fund

Creighton Court Redevelopment Phase I

Highland Grove Redevelopment Phase I

Building Back Healthier

Health Trust Equity Fund

Investing in our Future - Children and Families

Transforming community centers into opportunity centers for residents (multigenerational approach)

Child care and parental support

Family Crisis Funding

Parks Master Plan

TB Smith

Lucks Field

Calhoun

Southside Community Center

James River Branch Trail Purchase and Development (Connects Southside offroad to JRPS)

Crooked Branch Ravine Bridge - Connects Wythe to Fall Line Trail and Forest Hill Park

Texas Beach/North Bank Tower Repair (Connects Maymont Neighborhood to JRPS)

Property Acquisition for new Southside Parks (10 min walk gap)

Building Back Stronger

Small business grant application support and outreach

Façade and city beautification improvements (trees, signs, etc.)

OCWB Workforce Development and Community Ambassadors

CDFI Revolving Loan Fund

Covid-19 Administrative Response Reserve

Building Back Greener and more Resilient

Climate Risk Assessment and Implementation

Lead Line Replacement

Stormwater

Healthy Homes (Weatherization, Home Rehabilitation)

<i>Building Back Safer</i>
Gun violence prevention
First responders hazard pay
Enhanced Lighting (street and business) and cameras

	TOTAL ALLOCATION	YEAR 1 FUNDING	EXPENDITURES TO DATE	FUNDING AVAILABLE
	\$32,300,000	\$22,300,000	\$0	\$22,300,000
	\$20,000,000	\$10,000,000	\$0	\$10,000,000
	\$6,800,000	\$6,800,000	\$0	\$6,800,000
	\$5,500,000	\$5,500,000	\$0	\$5,500,000
	\$5,000,000	\$2,500,000	\$812,000	\$1,688,000
	\$5,000,000	\$2,500,000	\$812,000	\$1,688,000
	\$ 81,000,000	\$ 19,000,000	\$ 1,003,394	\$ 17,996,606
	\$2,000,000	\$2,000,000	\$748,519	1,251,481
	\$1,000,000	\$1,000,000	\$0	1,000,000
	\$500,000	\$500,000	\$0	500,000
	\$20,000,000	\$1,000,000	\$96,472	903,528
	\$20,000,000	\$1,000,000	\$99,842	900,158
	\$8,000,000	\$1,000,000	\$27,301	972,699
	\$16,000,000	\$8,000,000	\$15,627	7,984,373
	\$9,000,000	\$4,500,000	\$15,634	4,484,366
	\$1,000,000	-	-	-
	\$2,000,000	-	-	-
	\$1,500,000	-	-	-
	\$8,900,000	\$8,139,914	\$47,373	\$8,092,541
	\$1,000,000	\$1,000,000	\$47,373	\$952,627
	\$2,000,000	\$1,500,000	\$0	\$1,500,000
	\$1,500,000	\$1,500,000	\$0	\$1,500,000
	\$3,000,000	\$3,000,000	\$0	\$3,000,000
	\$1,400,000	\$1,139,914	\$0	\$1,139,914
	\$ 19,240,000	\$ 18,000,000	\$ 49,910	\$ 17,950,090
	\$1,540,000	\$300,000	\$49,910	\$250,090
	\$1,000,000	\$1,000,000	\$0	\$1,000,000
	\$12,500,000	\$12,500,000	\$0	\$12,500,000
	\$4,200,000	\$4,200,000	\$0	\$4,200,000

American Rescue Plan Act

City of Richmond

Build Back Better

Project Start Date: 10/14/2021

Scrolling Increment: 10

Total Category All

Total Category All

Milestone description	Category	Assigned to
Affordable Housing		
Mandatory Workshops	Milestone	Sheryl Hampton
First Notice of Funding Available (NOFA)	Milestone	Sheryl Hampton
Rating and Ranking of Applications	Milestone	Sheryl Hampton
Recommendation of Award and non-Award Notifications Sent	Milestone	Sheryl Hampton
O&R Adopted for ARPA Budget Reallocation/Amendment	On Track	Sheryl Hampton
Construction/Rehabilitation Recommendations	On Track	Sheryl Hampton
Distribution of Grant Awards/Agreements	On Track	Sheryl Hampton
New Grantee Workshop for next Tranche of Funding availability	On Track	Sheryl Hampton
Creighton Court		
HCD to draft agreement with the City Attorney's Office	On Track	Sheryl Hampton

Final draft agreements to be sent to RRHA	On Track	Sheryl Hampton
City Department, RRHA, and other related parties meeting	On Track	Sheryl Hampton
Acquire necessary permits	Milestone	Sheryl Hampton
Abatement/Demo	Milestone	Sheryl Hampton
Selection of Water/Sewer Contractor	Milestone	Sheryl Hampton
Infrastructure Work and Completion	Milestone	Sheryl Hampton
Highland Grove		
HCD to coordinate a meeting between external and internal development team (DPW, DPU, and PDR) to identify roles	On Track	Sheryl Hampton
Feedback on the Preliminary Plat Review	On Track	Sheryl Hampton
Complete subdivision	Milestone	Sheryl Hampton
Community Outreach	Milestone	Sheryl Hampton
Infrastructure Work and Completion	Milestone	Sheryl Hampton

Legend:

On track

Low

location (Tranche 1):	22,300,000
Expenditure To-Date	-

Progress	Start	Days	End
			0
100%	12/2/2021	7	12/9/2021
100%	12/10/2021	31	1/10/2022
100%	2/1/2022	27	2/28/2022
100%	3/24/2022	4	3/28/2022
100%	3/28/2022	15	4/12/2022
100%	4/25/2022	30	5/25/2022
50%	5/1/2022	60	6/30/2022
0%	11/1/2022	60	12/31/2022
100%	3/1/2022	45	4/15/2022

[illegible]

100%	4/30/2022	15	5/15/2022
Ongoing	5/10/2022	30	Ongoing
50%	5/1/2022	244	12/31/2022
75%	5/2/2022	151	9/30/2022
30%	7/1/2022	122	10/31/2022
0%	9/1/2022	850	12/29/2024

Ongoing	4/1/2022	30	Ongoing
50%	2/15/2022	45	4/1/2022
0%	4/1/2022	215	11/2/2022
0%	5/1/2022	200	11/17/2022
0%	11/1/2022	790	12/30/2024

▶	▶	▶	▶	▶	▶	▶
▶	▶					
▶	▶	▶	▶	▶	▶	▶


risk

Med risk


High risk

Unassigned

[illegible]

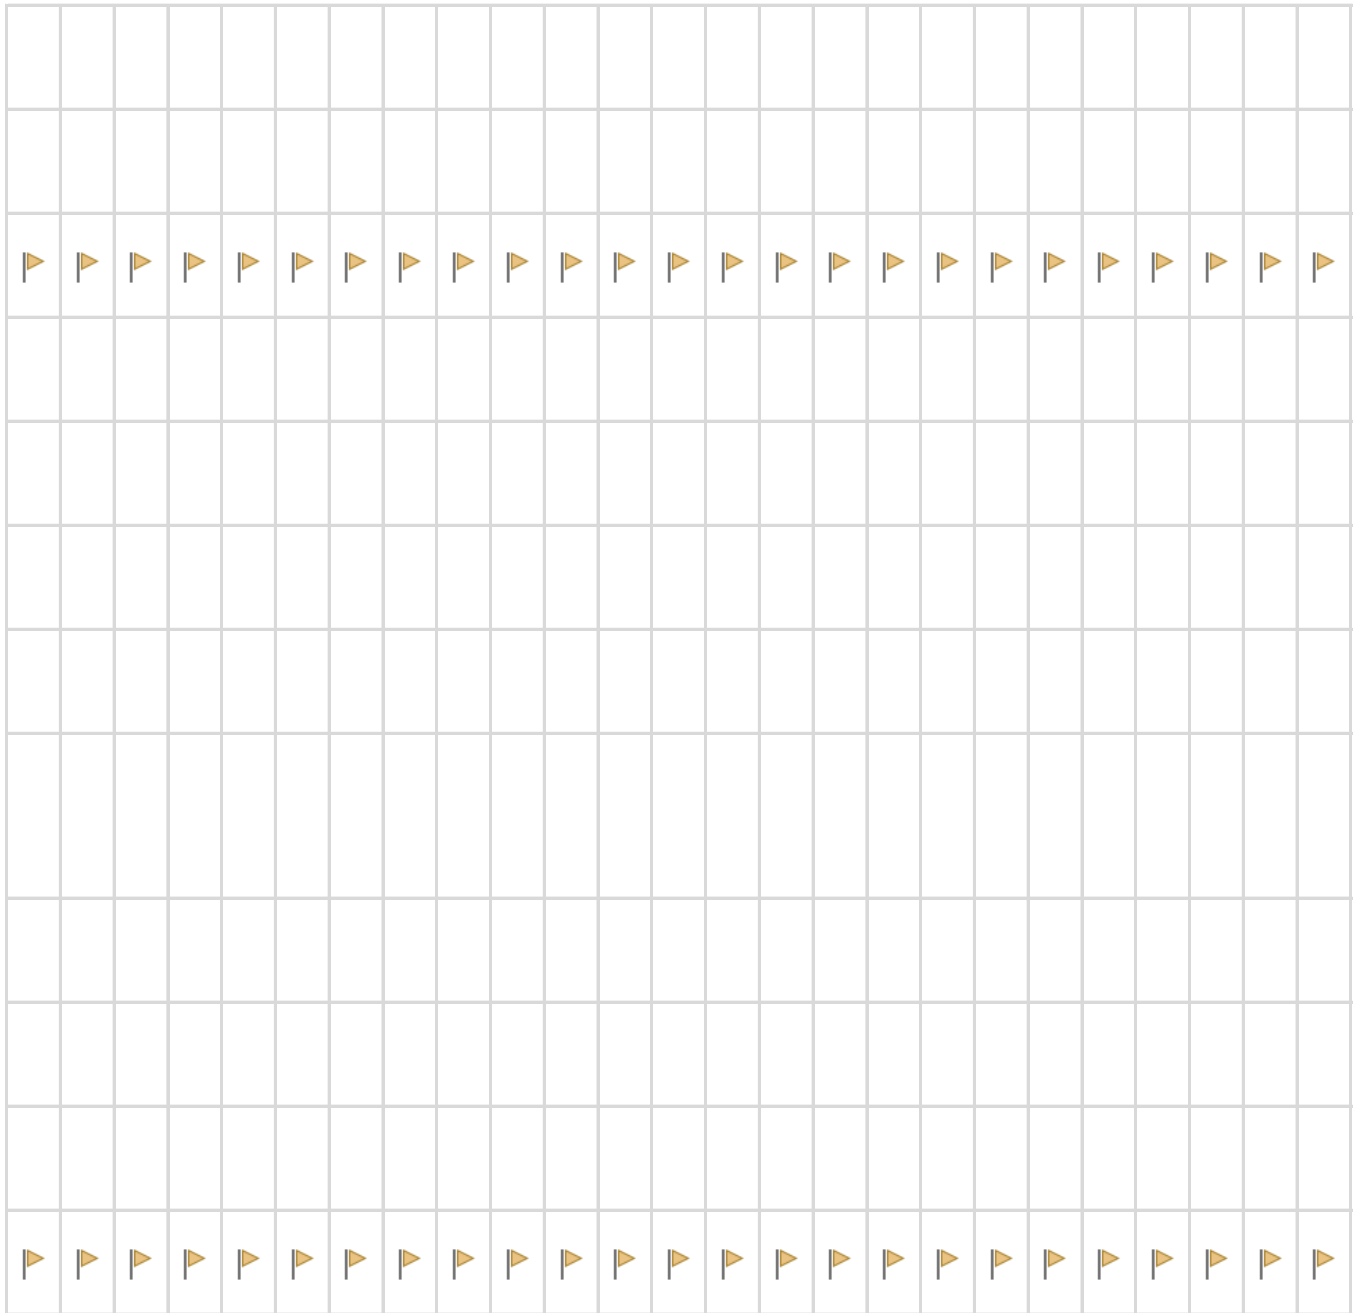

[illegible]

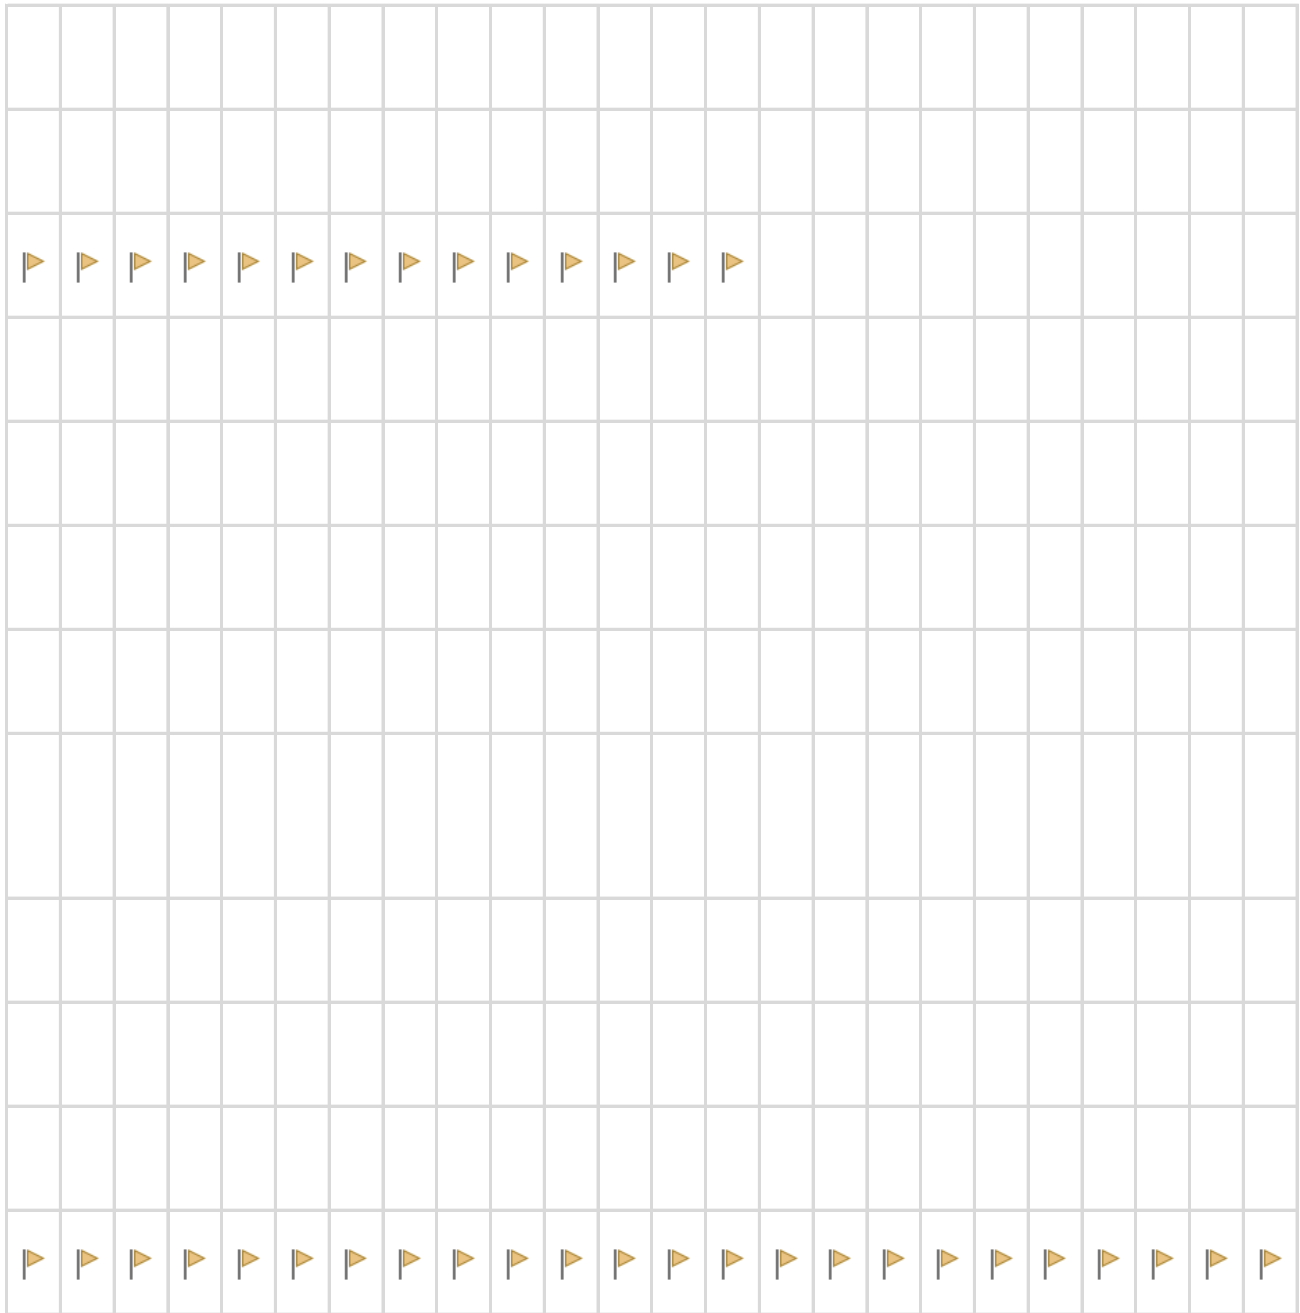



American Rescue Plan Act

City of Richmond

Build Back Healthier

Project Start Date: 10/14/2021

Scrolling Increment: 0

Total Category All

Total Category E

Milestone description	Category	Assigned to
Health Equity Trust Fund		
Identification of external partner (RCHD) to execute fund	On Track	Maggie Anderson
Creation of MOU and approval by City Council	On Track	Maggie Anderson
Execution of MOU	Milestone	Maggie Anderson
Advisory Committee Formed via RCHD	Goal	Ruth Morrison
First Plan Submitted to the City (following MOU)	Milestone	Ruth Morrison
Award Funds (and then cycle continues)	Milestone	Ruth Morrison

ocation (Tranche 1):	2,500,000
penditure To-Date	812,000

Progress	Start	Days	End
			0
100%	10/14/2021	180	4/12/2022
100%	1/1/2022	90	4/1/2022
100%	3/29/2022	15	4/13/2022
100%	4/1/2022	30	5/1/2022
100%	5/1/2022	90	7/30/2022
50%	6/1/2022	90	8/30/2022

Legend:

On track

Low

[illegible]

risk

Med risk

High risk

Unassigned

[illegible]

[illegible]



American Rescue Plan Act

City of Richmond

Investing in our Children

Project Start Date: 10/14/2021

Scrolling Increment: 18

Total Category All

Total Category I

Milestone description	Category	Assigned to
Child Care and Parental Supports		
Child Care & Preschool Stabilization and Expansion Grant Solicitation/Awards	On Track	Eva Colen
Partner Identified/Announced for other \$500,000 Stabilization & Expansion Funds	On Track	Eva Colen
Partner Identified/Announced for Home Visiting Expansion Grant	On Track	Eva Colen
Partner Identified/Announced for UPK Cost Modeling Study	On Track	Eva Colen
Contracts Executed for Stabilization & Expansion Grants, Home Visiting, and UPK Cost Modeling Study	On Track	Eva Colen
Universal Preschool (UPK) Cost Modeling Study	On Track	Eva Colen
Universal Preschool (UPK) Revenue Options Memo	On Track	Eva Colen
Children's Museum Access Grant	On Track	Eva Colen
RPS Preschool Aftercare	On Track	Eva Colen

Out of School Time Landscape Analysis	On Track	Eva Colen
Family Crisis Funding		
Finalize Family Eligibility Criteria	Low Risk	Reggie Gordon
Identify Provider Partners who will be qualified to enroll families	On Track	Reggie Gordon
Finalize spend plan and timeline	Low Risk	Reggie Gordon
Soft launch with first partners and families	Milestone	Reggie Gordon
Public launch	Milestone	Reggie Gordon
Parks Master Plan		
Creation and release of RFP	Med Risk	Chris Frelke
Firm section	Milestone	Chris Frelke
Internal planning team established	On Track	Chris Frelke
Community Advisory Board feedback	On Track	Chris Frelke
Draft Plan Review	Milestone	Chris Frelke
Planning Commission and City Council adoption	Goal	Chris Frelke
TB Smith		
Release of internal engagement and conceptual planning task order	Milestone	Chris Frelke
Selection of engagement team	Milestone	Chris Frelke

Engagement process and conceptual designs complete	Milestone	Chris Frelke
Construction documents phase	On Track	Chris Frelke
Final UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke
All construction complete	Goal	Chris Frelke
Lucks Field		
Release of internal engagement and conceptual planning task order	Milestone	Chris Frelke
Selection of engagement team	Milestone	Chris Frelke
Engagement process and conceptual designs complete	Milestone	Chris Frelke
Construction documents phase	On Track	Chris Frelke
Final UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke
All construction complete	Goal	Chris Frelke
Calhoun		
Finalize and execute agreement with RRHA for transfer of Calhoun to PRCF	Milestone	Chris Frelke
Complete community-engaged design process with residents	Milestone	Chris Frelke
Construction document phase	Milestone	Chris Frelke
Final UDC, Planning Commission, and City Council approvals	Milestone	Chris Frelke
All construction complete	Goal	Chris Frelke

Southside Community Center		
Final Design Documents	On Track	Chris Frelke
Final UDC and Planning Commission approvals	Milestone	Chris Frelke
Final City Council approval	Milestone	Chris Frelke
All construction complete	Goal	Chris Frelke
James River Branch Trail Purchase and Development		
CSX negotiations with local and state partners	Milestone	Chris Frelke
Land acquisition/lease/or recreational lease agreement	Milestone	Chris Frelke
Final design documents, UDC, Planning Commission, permitting and City Council approvals	Milestone	Chris Frelke
All construction complete	Milestone	Chris Frelke
Crooked Branch Ravine Bridge		
Final design documents and UDC, Planning Commission and Council approvals	Milestone	Chris Frelke
Public Engagement Process	Milestone	Chris Frelke
All construction complete	Milestone	Chris Frelke
Texas Beach/North Bank Tower Repair		
Site investigation and CSX negotiations	Milestone	Chris Frelke
Site selection and design and engineering document creation and CSX	Milestone	Chris Frelke

Final design documents, UDC, Planning Commission and City Council approvals	Milestone	Chris Frelke
All construction complete	Milestone	Chris Frelke
Property Acquisition for new Southside Parks		
Updated land identification criteria	On Track	Chris Frelke
Solidified land trust and non-profit partnerships	Milestone	Chris Frelke
Negotiation process established	Milestone	Chris Frelke
Funding leverage opportunities identified	Milestone	Chris Frelke
Land acquired	Goal	Chris Frelke

location (Tranche 1):	19,000,000
Expenditure To-Date	1,003,394

Progress		Start	Days	End
100%		2/16/2022	90	5/17/2022
100%		1/10/2022	30	2/9/2022
100%		3/7/2022	30	4/6/2022
100%		2/1/2022	90	5/2/2022
90%		4/1/2022	260	12/17/2022
25%		8/1/2022	300	5/28/2023
90%		8/1/2022	90	10/30/2022
100%		5/15/2022	120	9/12/2022
80%		8/1/2022	60	9/30/2022

Legend:

On track

Low

[illegible]


risk

Med risk


High risk


Unassigned


[illegible]

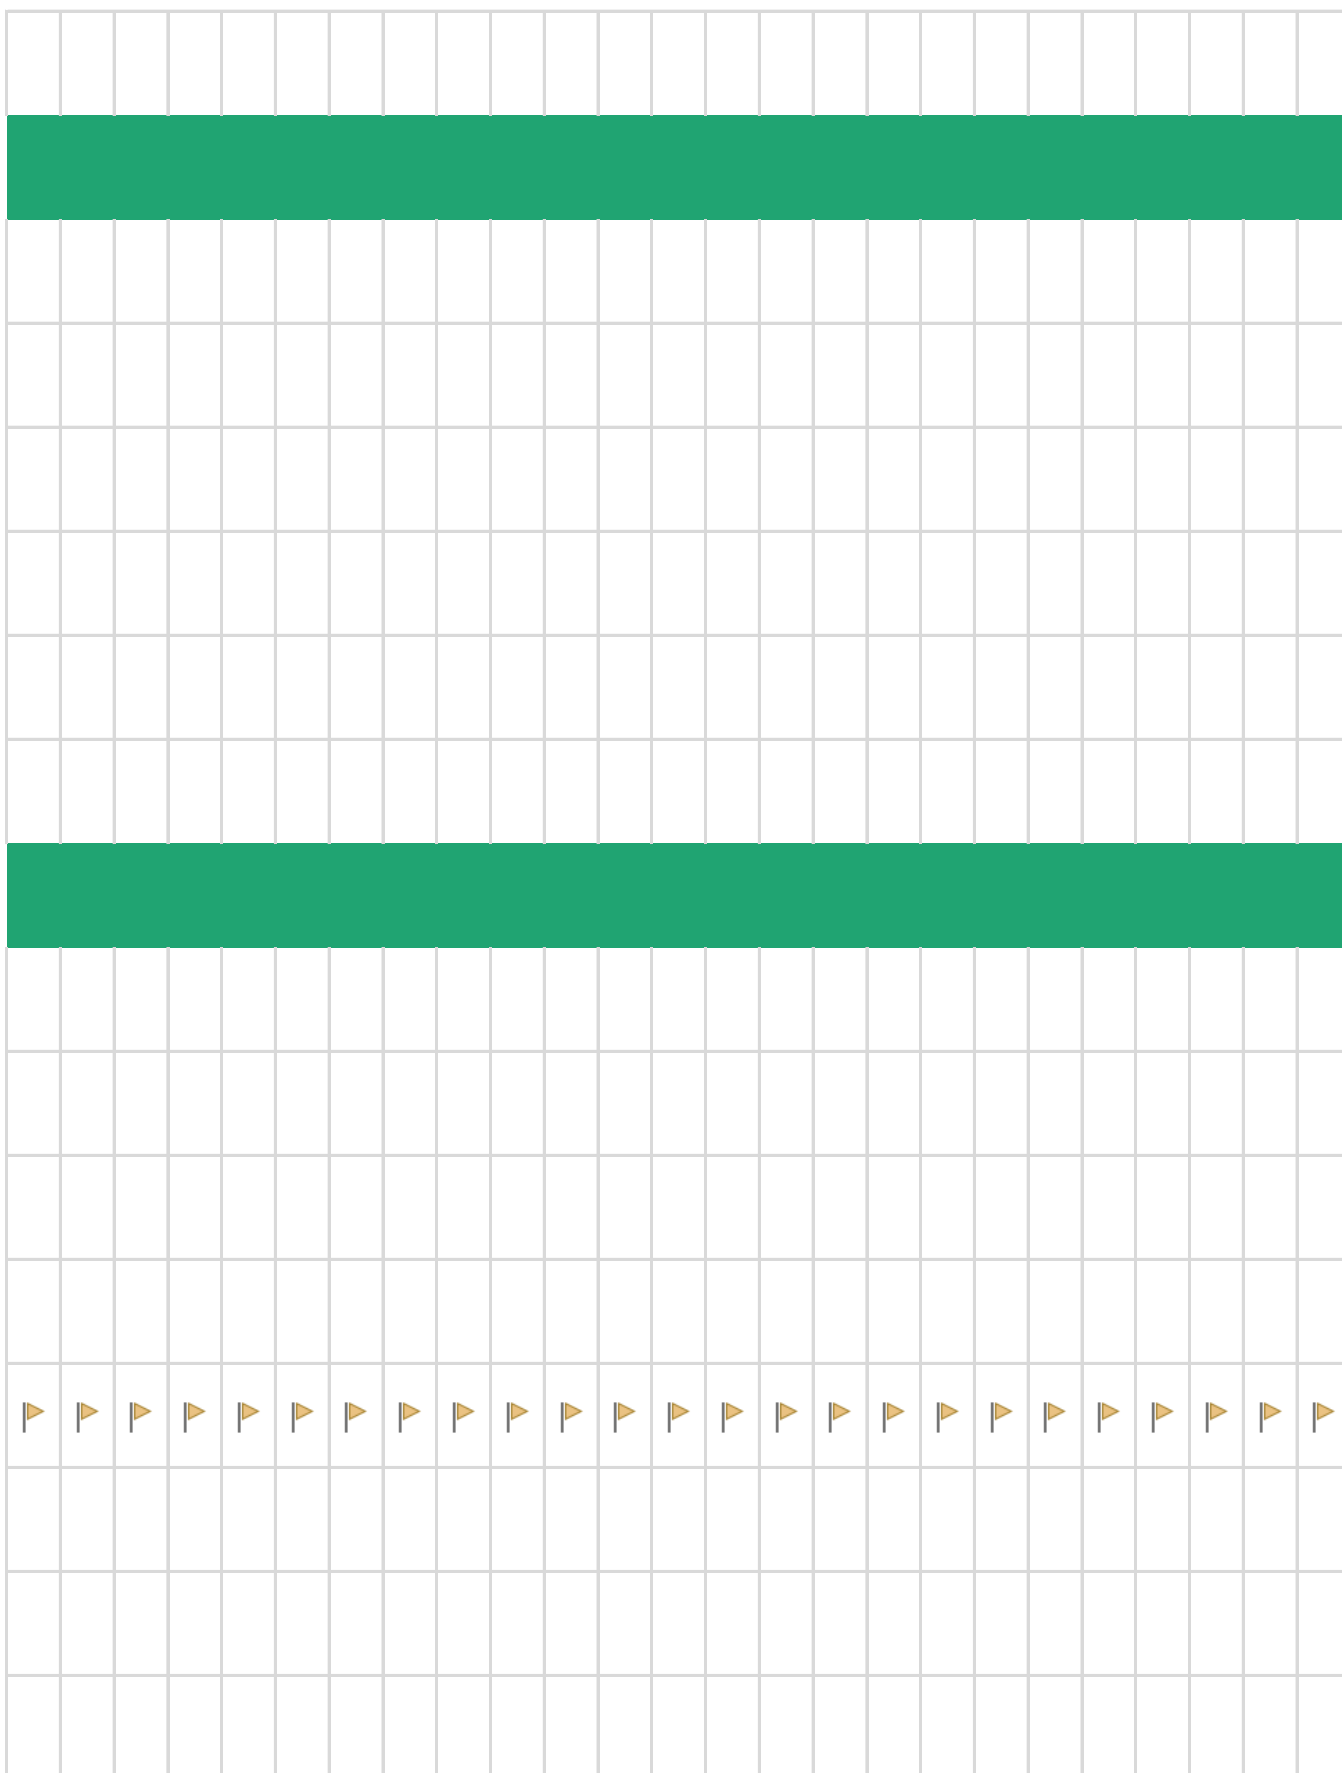

[illegible]

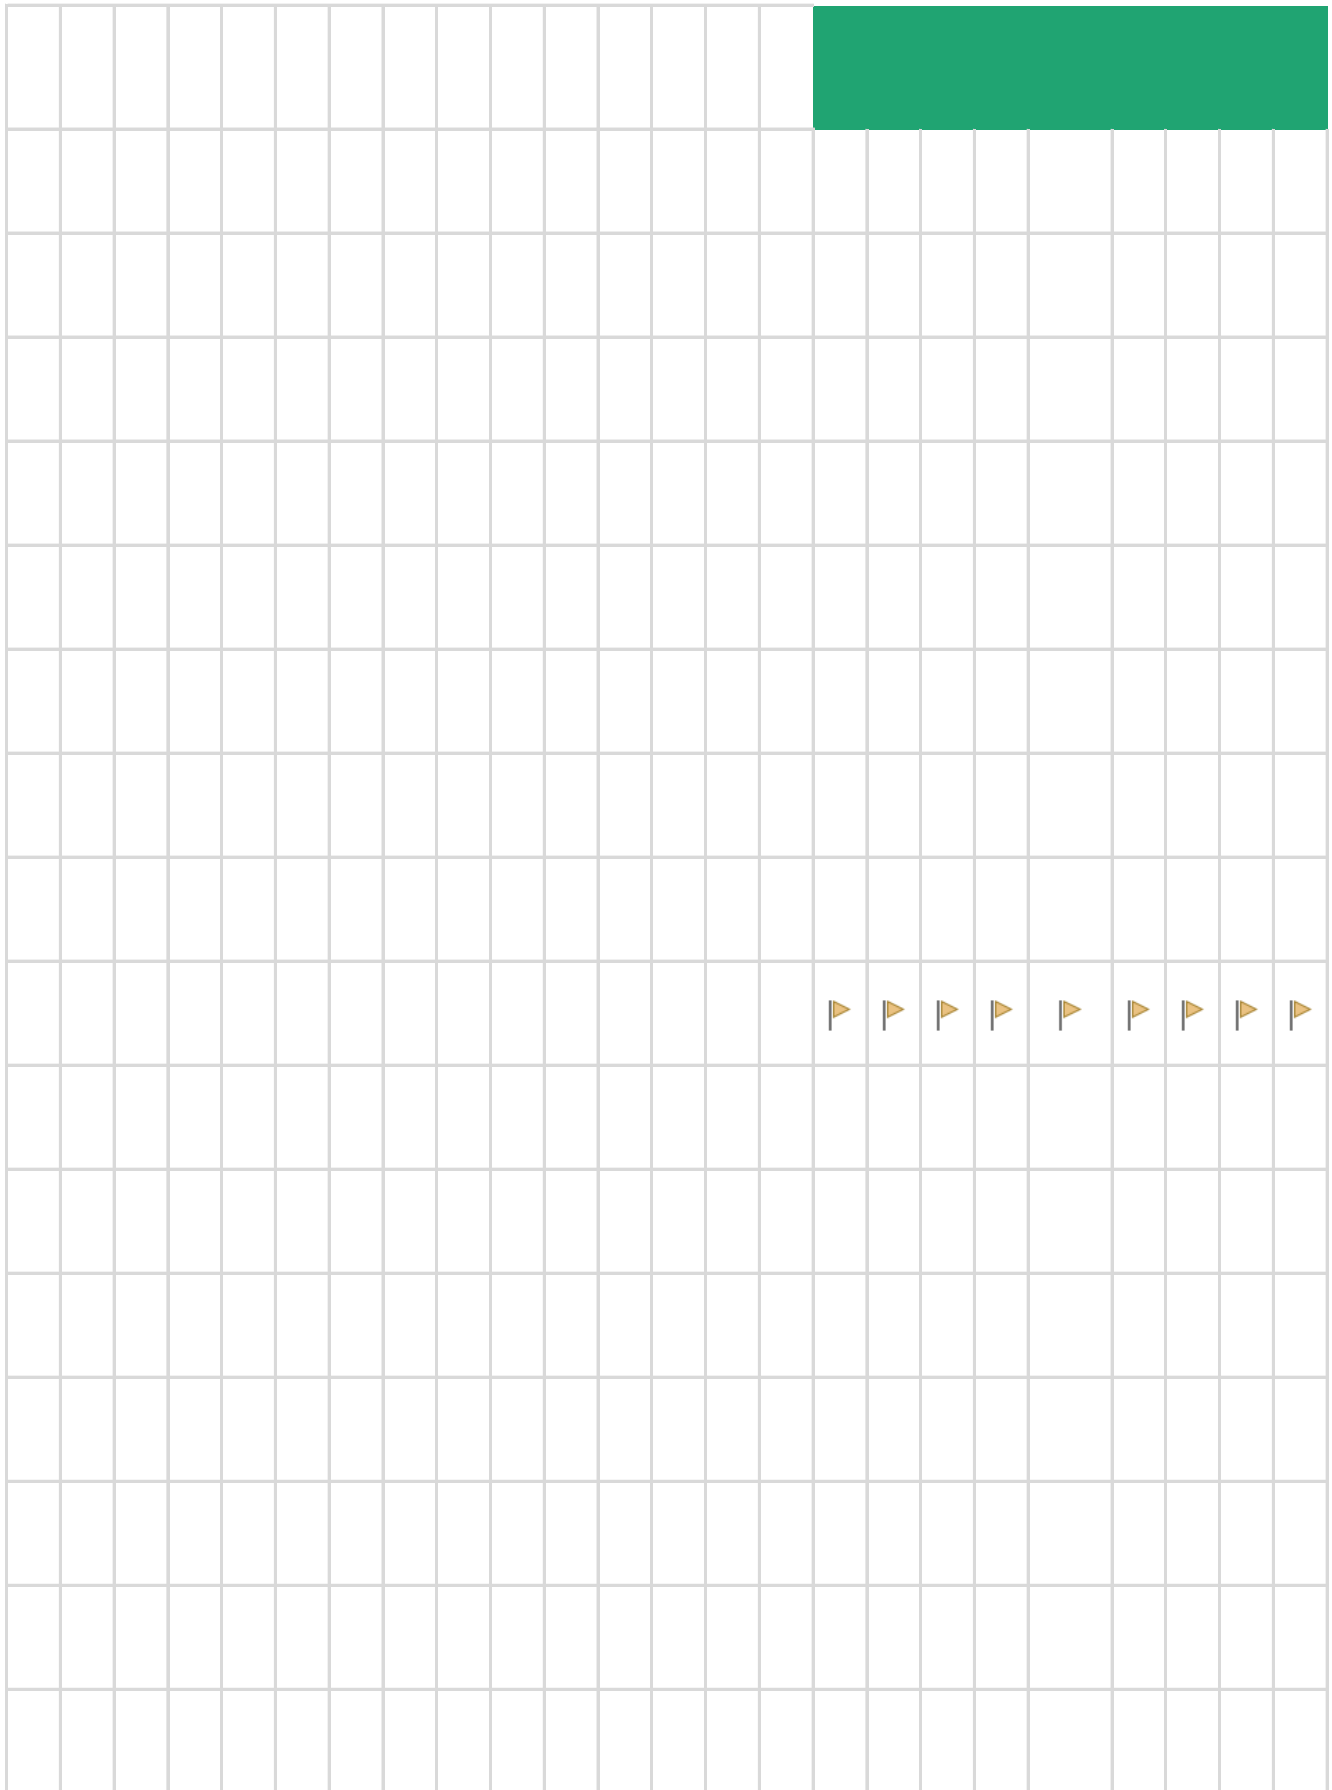

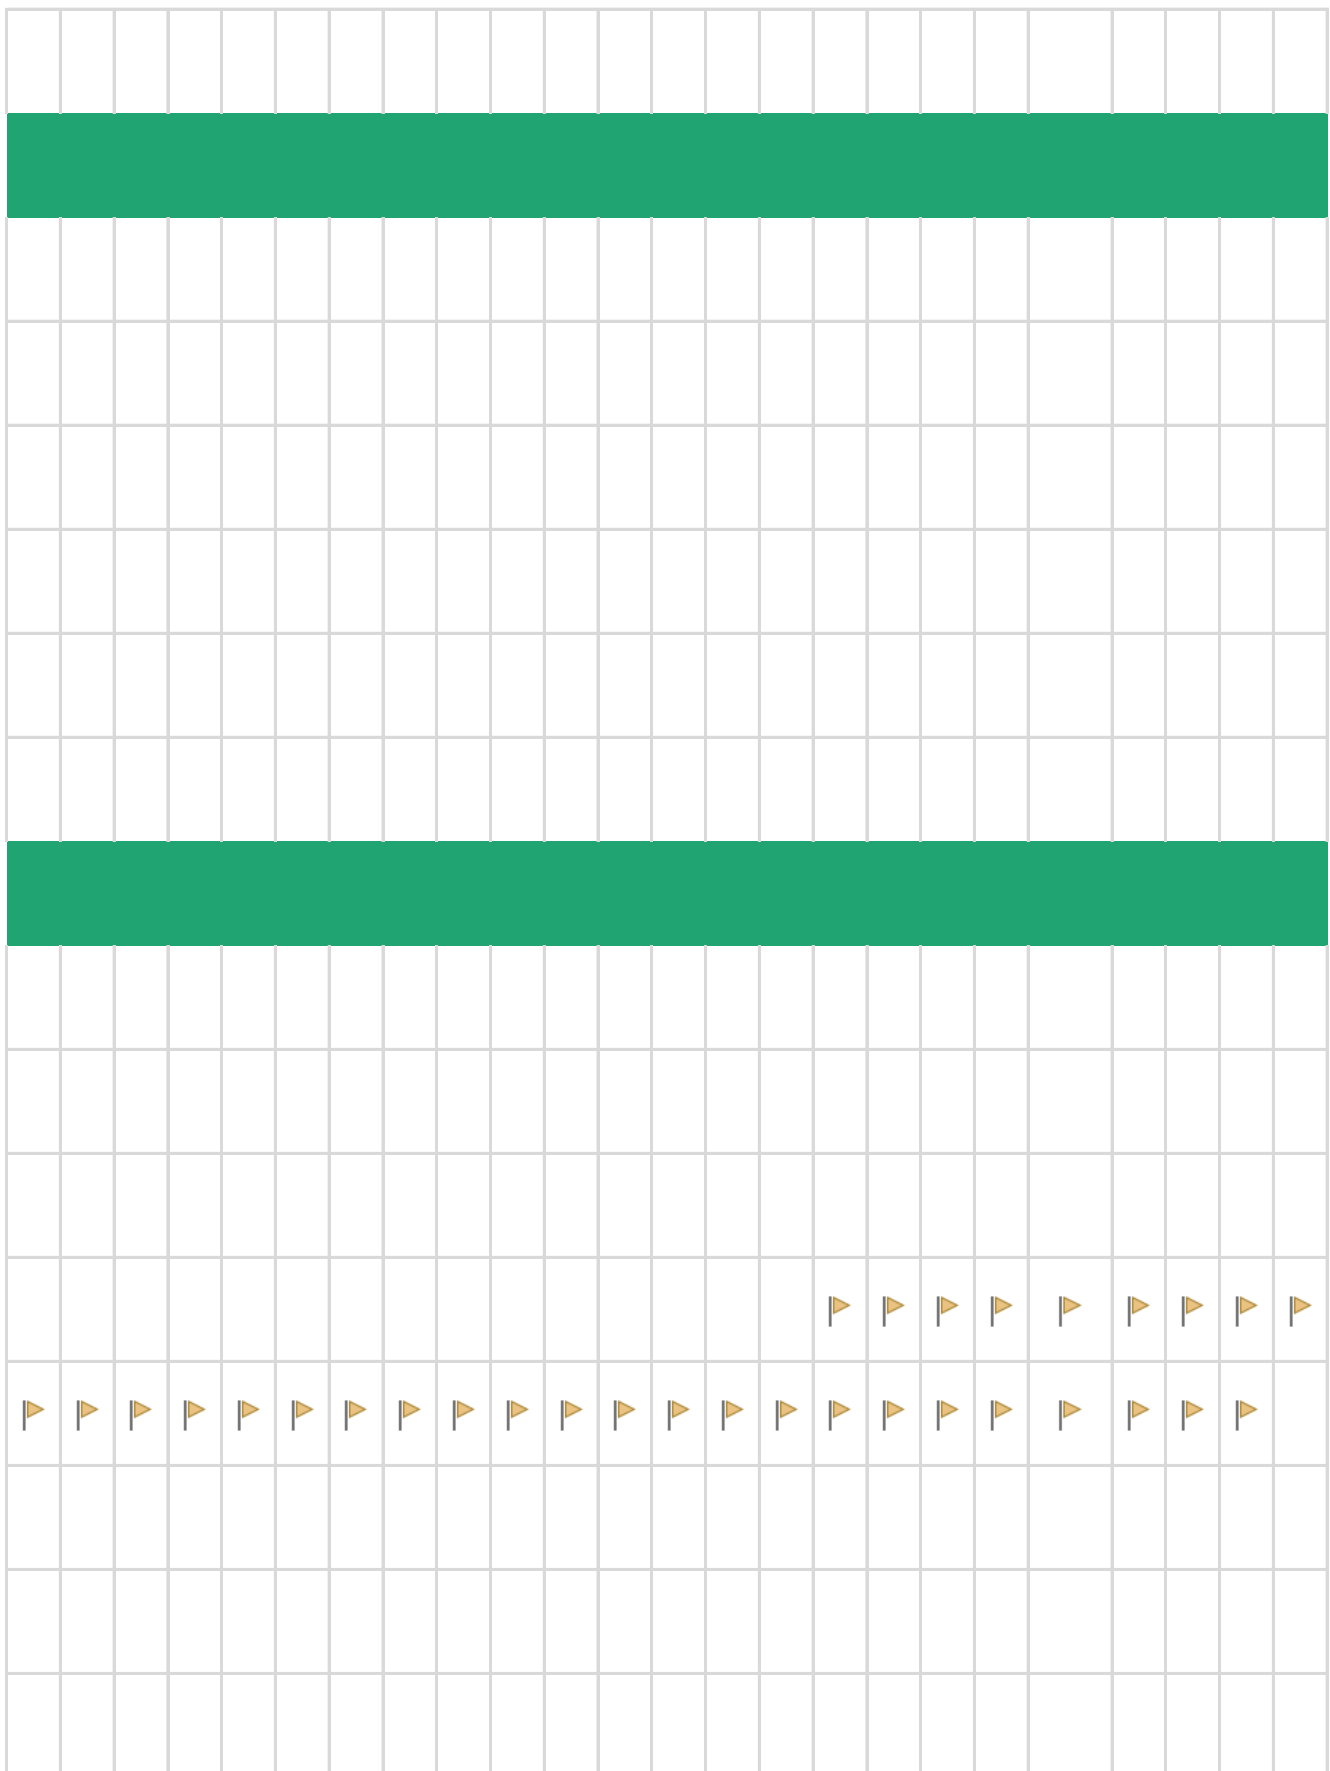

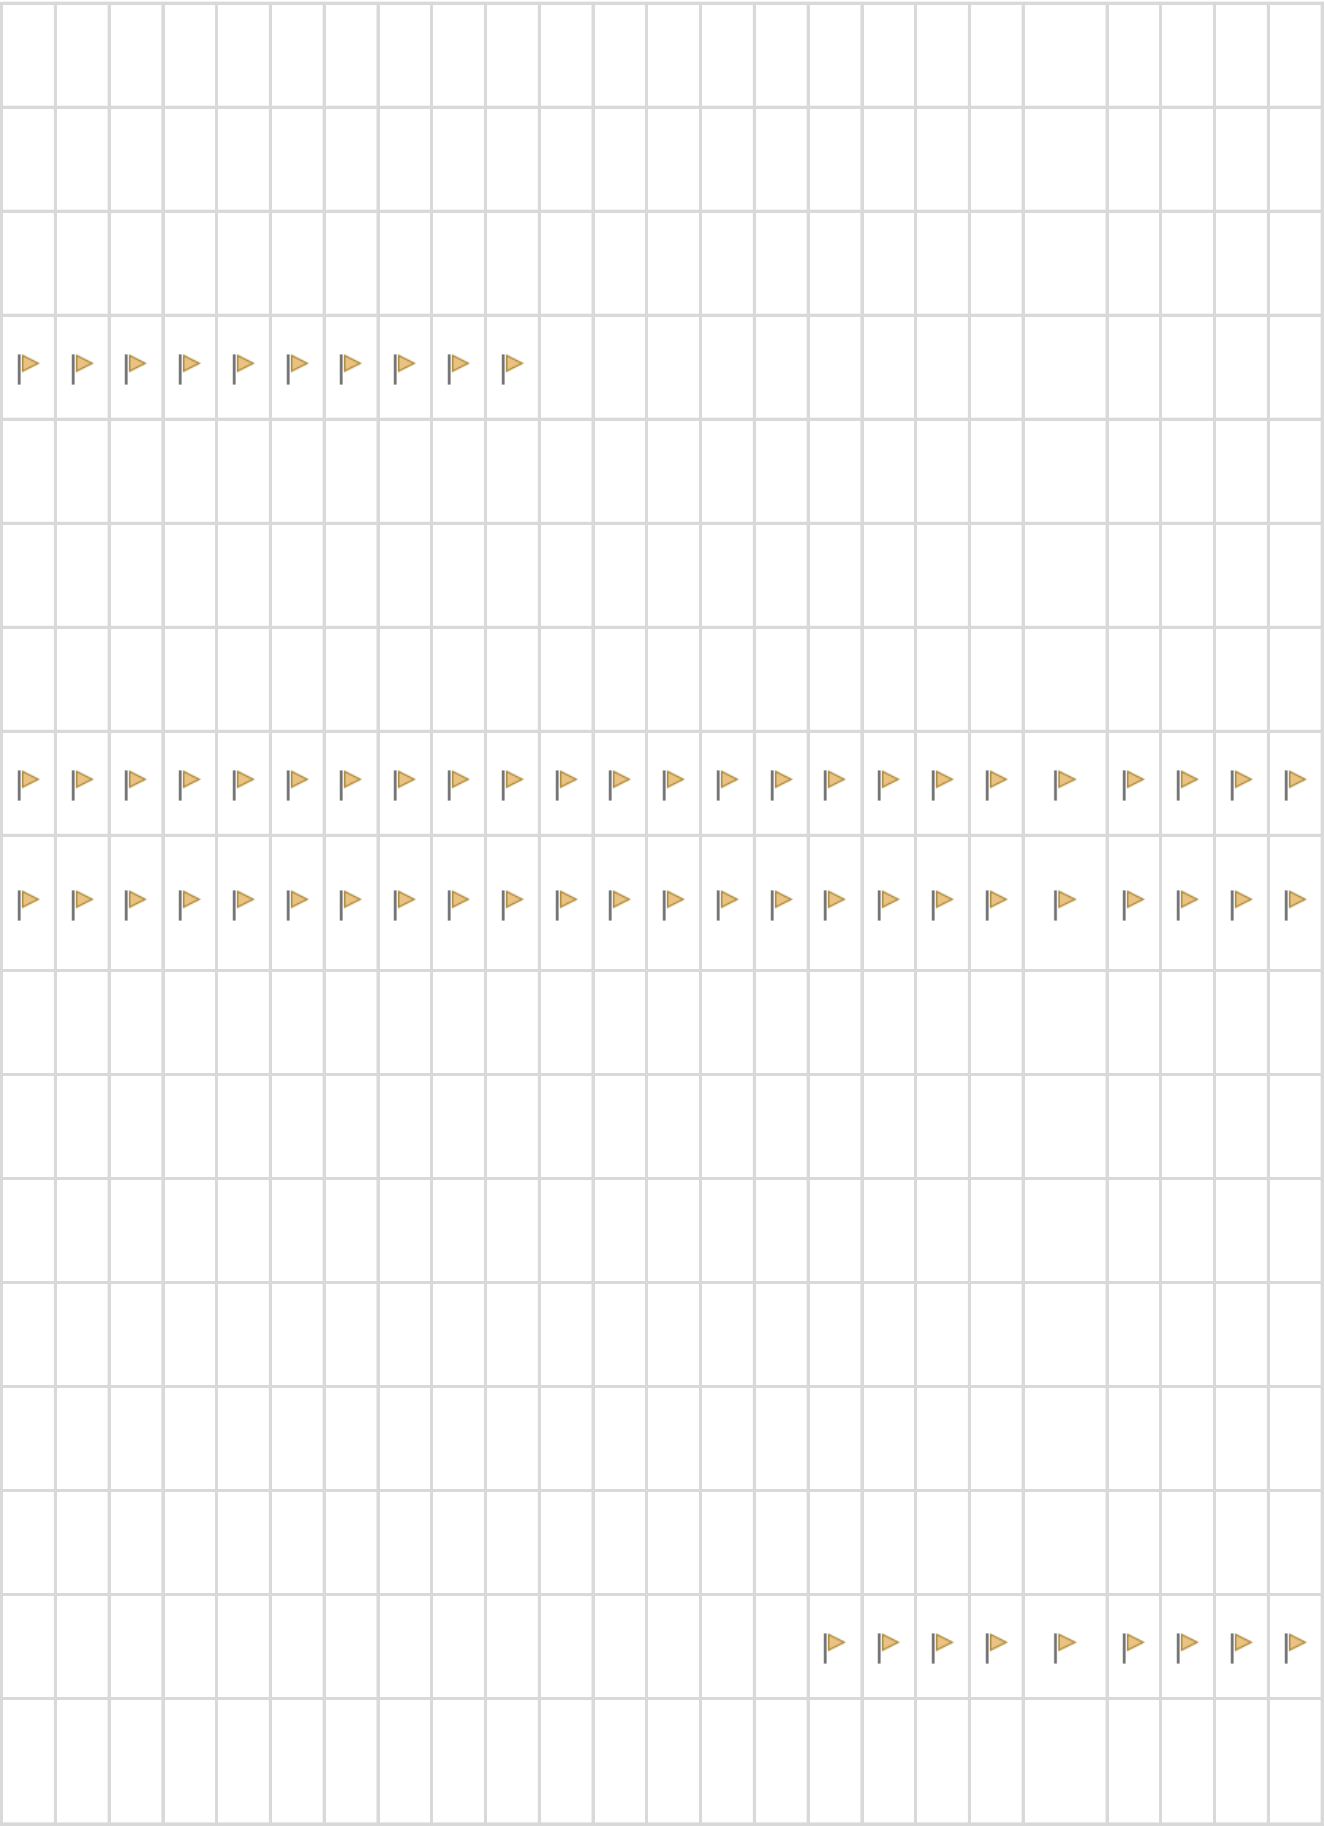



American Rescue Plan Act

City of Richmond

Build Back Stronger

Project Start Date: 10/14/2021

Scrolling Increment: 12

Total Category A
Total Category

Milestone description	Category	Assigned to
Small Business Grant Application		
Develop program scope of work	On Track	Pat Foster
Identified potential partners, service providers and business participants	On Track	Pat Foster
Select business participants	On Track	Pat Foster
Start implementation of Triple A program of assessing , developing their respective strategy and	On Track	Pat Foster
Have at least 5 businesses in the pipeline	Goal	Pat Foster
Have at least 10 business receive necessary resources	Goal	Pat Foster
Have at least 20 businesses receive necessary resources	Goal	Pat Foster
Façade and City Beautification		
Review Design Proposal-consultant to review 20 locations	On Track	Torrence Robinson
Notice to Proceed w/Design	Milestone	Torrence Robinson

Complete Design	Milestone	Torrence Robinson
Public Engagement and Outreach	Milestone	Torrence Robinson
Construction Start	Milestone	Torrence Robinson
Complete Construction and project close out	Milestone	Torrence Robinson
OCWB Workforce Development & Community Ambassadors		
Exploring partnerships for Returning Citizen Guaranteed Income Pilot program (age 18+ eligible)	On Track	Reggie Gordon
Launch of Returning Citizen Guaranteed Income Pilot Program	On Track	Reggie Gordon
Planning and design of Workforce Development/skilled trades//Employment Services for 18-24 year olds (Builds off MYA model)	On Track	Reggie Gordon
Mayor Youth Academy Expansion - Applications	On Track	Reggie Gordon
Skills and Trade Development Programs (OCWB Model)	On Track	Reggie Gordon
OCWB Ambassadors	On Track	Reggie Gordon
CDFI Revolving Loan		
Received approval of planned utilization of funds	On Track	Pat Foster
Update:Prepare solicitations for service providers. Solicitation will no longer be needed. Grants will be given to qualified CDFI(s).	On Track	Pat Foster
Program Assessment	On Track	Pat Foster

Selection of CDFI(s)	Milestone	Pat Foster
Draft MOU/Contracts	Milestone	Pat Foster
Implementation of the Program	Milestone	Pat Foster
OOVID - 19 Administration Reponse Reserve		
Task 1 - TBD		Shelia White/Jason May
Task 2 - TBD		Shelia White/Jason May
Task 3 - TBD		Shelia White/Jason May
Task 4 - TBD		Shelia White/Jason May
Task 5 - TBD		Shelia White/Jason May

Allocation (Tranche 1):	8,139,914
Expenditure To-Date	47,373

Legend:

On track

Low

Progress	Start	Days	End
			0
100%	1/10/2022	15	1/25/2022
95%	2/1/2022	333	12/31/2022
95%	4/15/2022	260	12/31/2022
20%	5/2/2022	213	12/1/2022
100%	6/1/2022	30	7/1/2022
0%	7/15/2022	169	12/31/2022
0%	7/15/2022	169	12/31/2022
100%	1/1/2022	100	4/11/2022
0%	8/1/2022	90	10/30/2022

[illegible]

	0%	12/19/2022	252	8/28/2023
	0%	4/18/2023	60	6/17/2023
	0%	6/17/2023	120	10/15/2023
	0%	1/1/2024	120	4/30/2024
	33%	4/1/2022	210	10/28/2022
	0%	6/1/2022	150	10/29/2022
	40%	3/1/2022	250	11/6/2022
	100%	3/1/2022	30	3/31/2022
	10%	8/1/2022	120	11/29/2022
	On-Going	1/1/2022	1,095	12/31/2024
	100%	3/21/2022	1	3/22/2022
	25%	4/1/2022	212	10/30/2022
	20%	5/1/2022	182	10/30/2022

33%	4/1/2022	210	10/28/2022
--------------------------------------	----------	-----	------------

0%	6/1/2022	150	10/29/2022
----	----------	-----	------------

40%	3/1/2022	250	11/6/2022
-----	----------	-----	-----------

100%	3/1/2022	30	3/31/2022
------	----------	----	-----------

10%	8/1/2022	120	11/29/2022
-----	----------	-----	------------

On-Going	1/1/2022	1,095	12/31/2024
----------	----------	-------	------------

100%	3/21/2022	1	3/22/2022
------	-----------	---	-----------

25%	4/1/2022	212	10/30/2022
-----	----------	-----	------------

20%	5/1/2022	182	10/30/2022
-----	----------	-----	------------

A blank sheet of graph paper with a grid of squares. A vertical red line runs down the left side, and a horizontal green bar highlights the bottom row.

	25%	11/30/2022	30	12/30/2022
--	-----	------------	----	------------

0%	12/1/2022	30	12/31/2022
----	-----------	----	------------

0%	1/10/2023	356	1/1/2024
----	-----------	-----	----------

1/1/2023

1/1/2023

1/1/2023

1/1/2023

1/1/2023

[illegible]


risk

Med risk

High risk


Unassigned


[illegible]

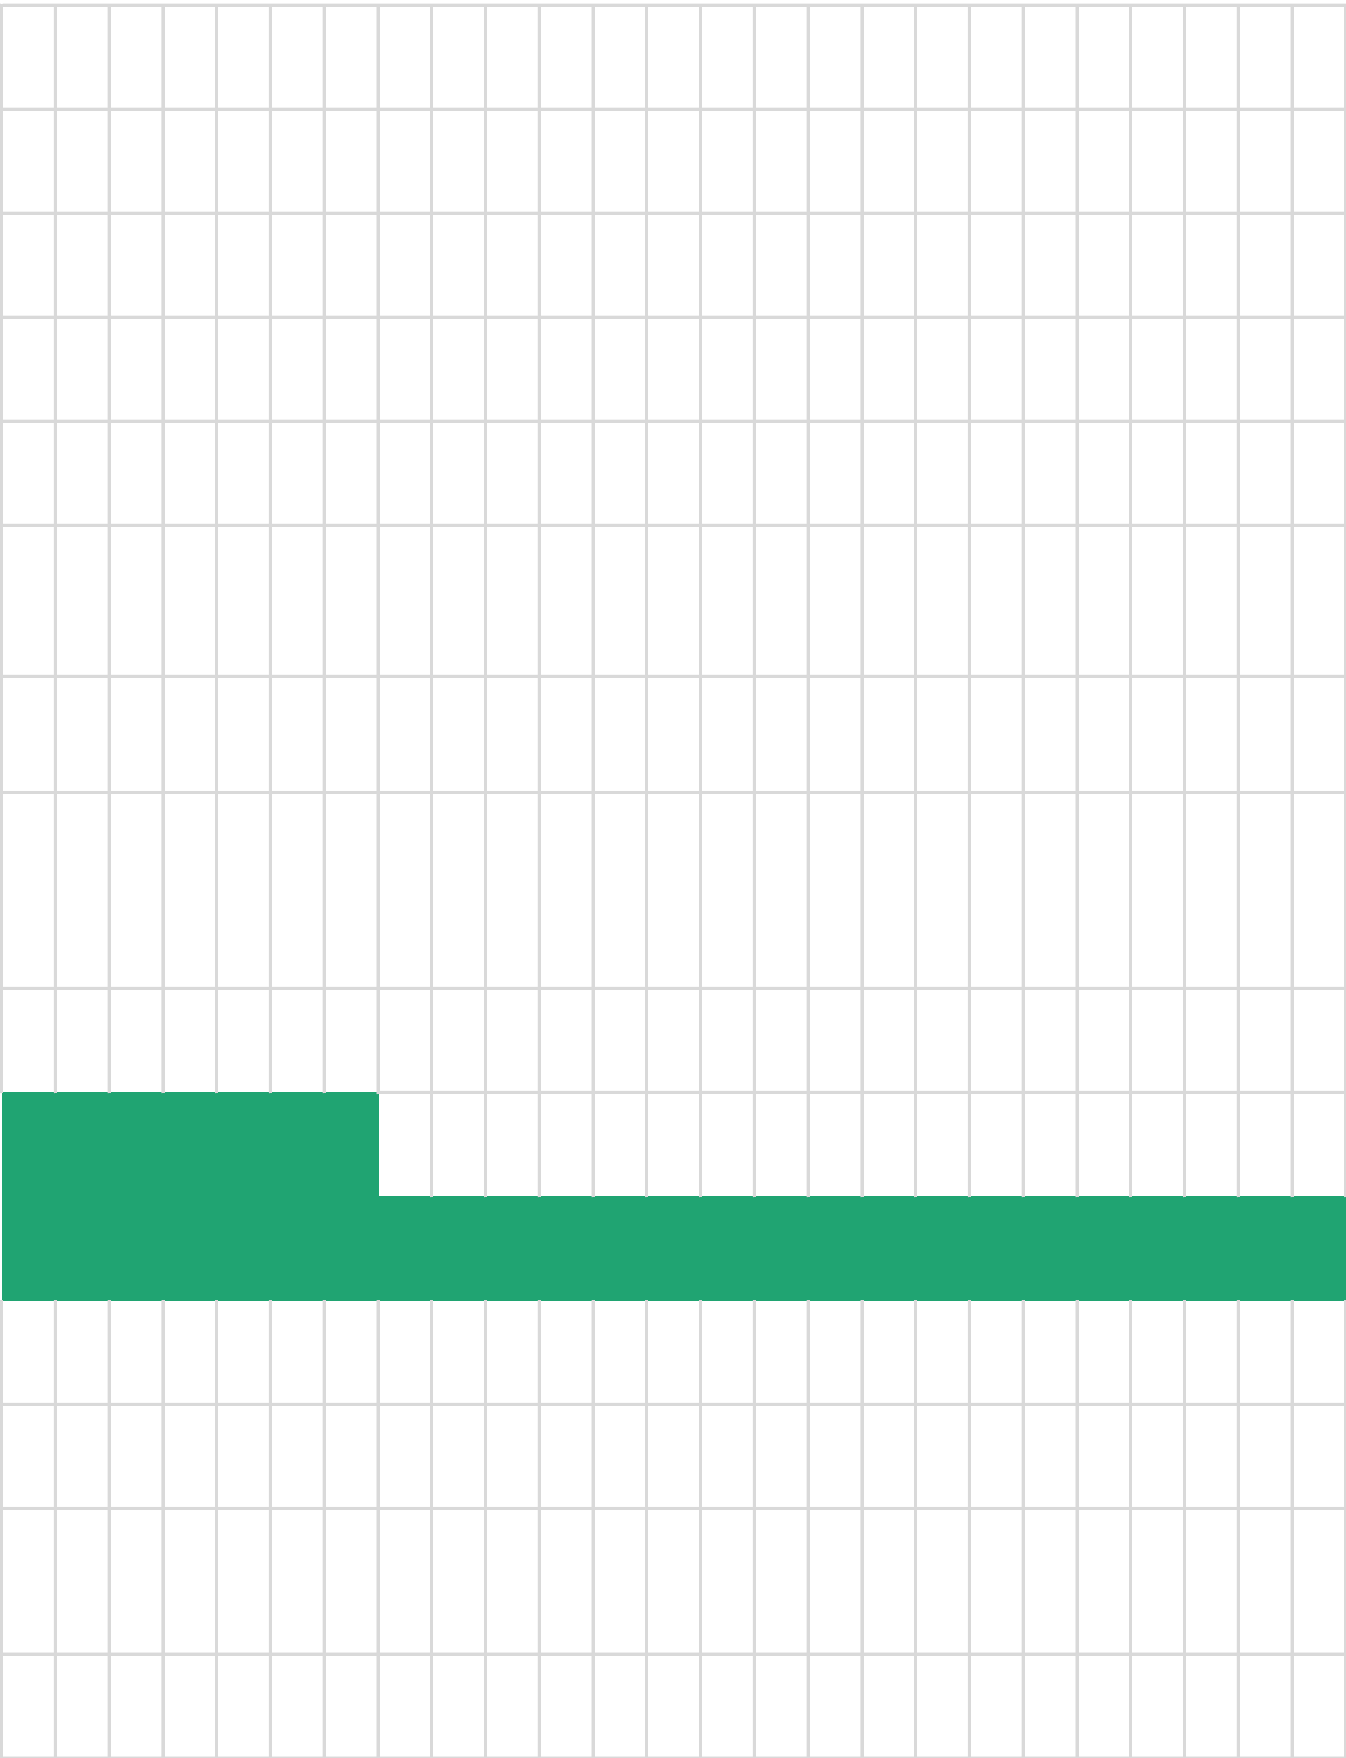

[illegible]

[illegible]

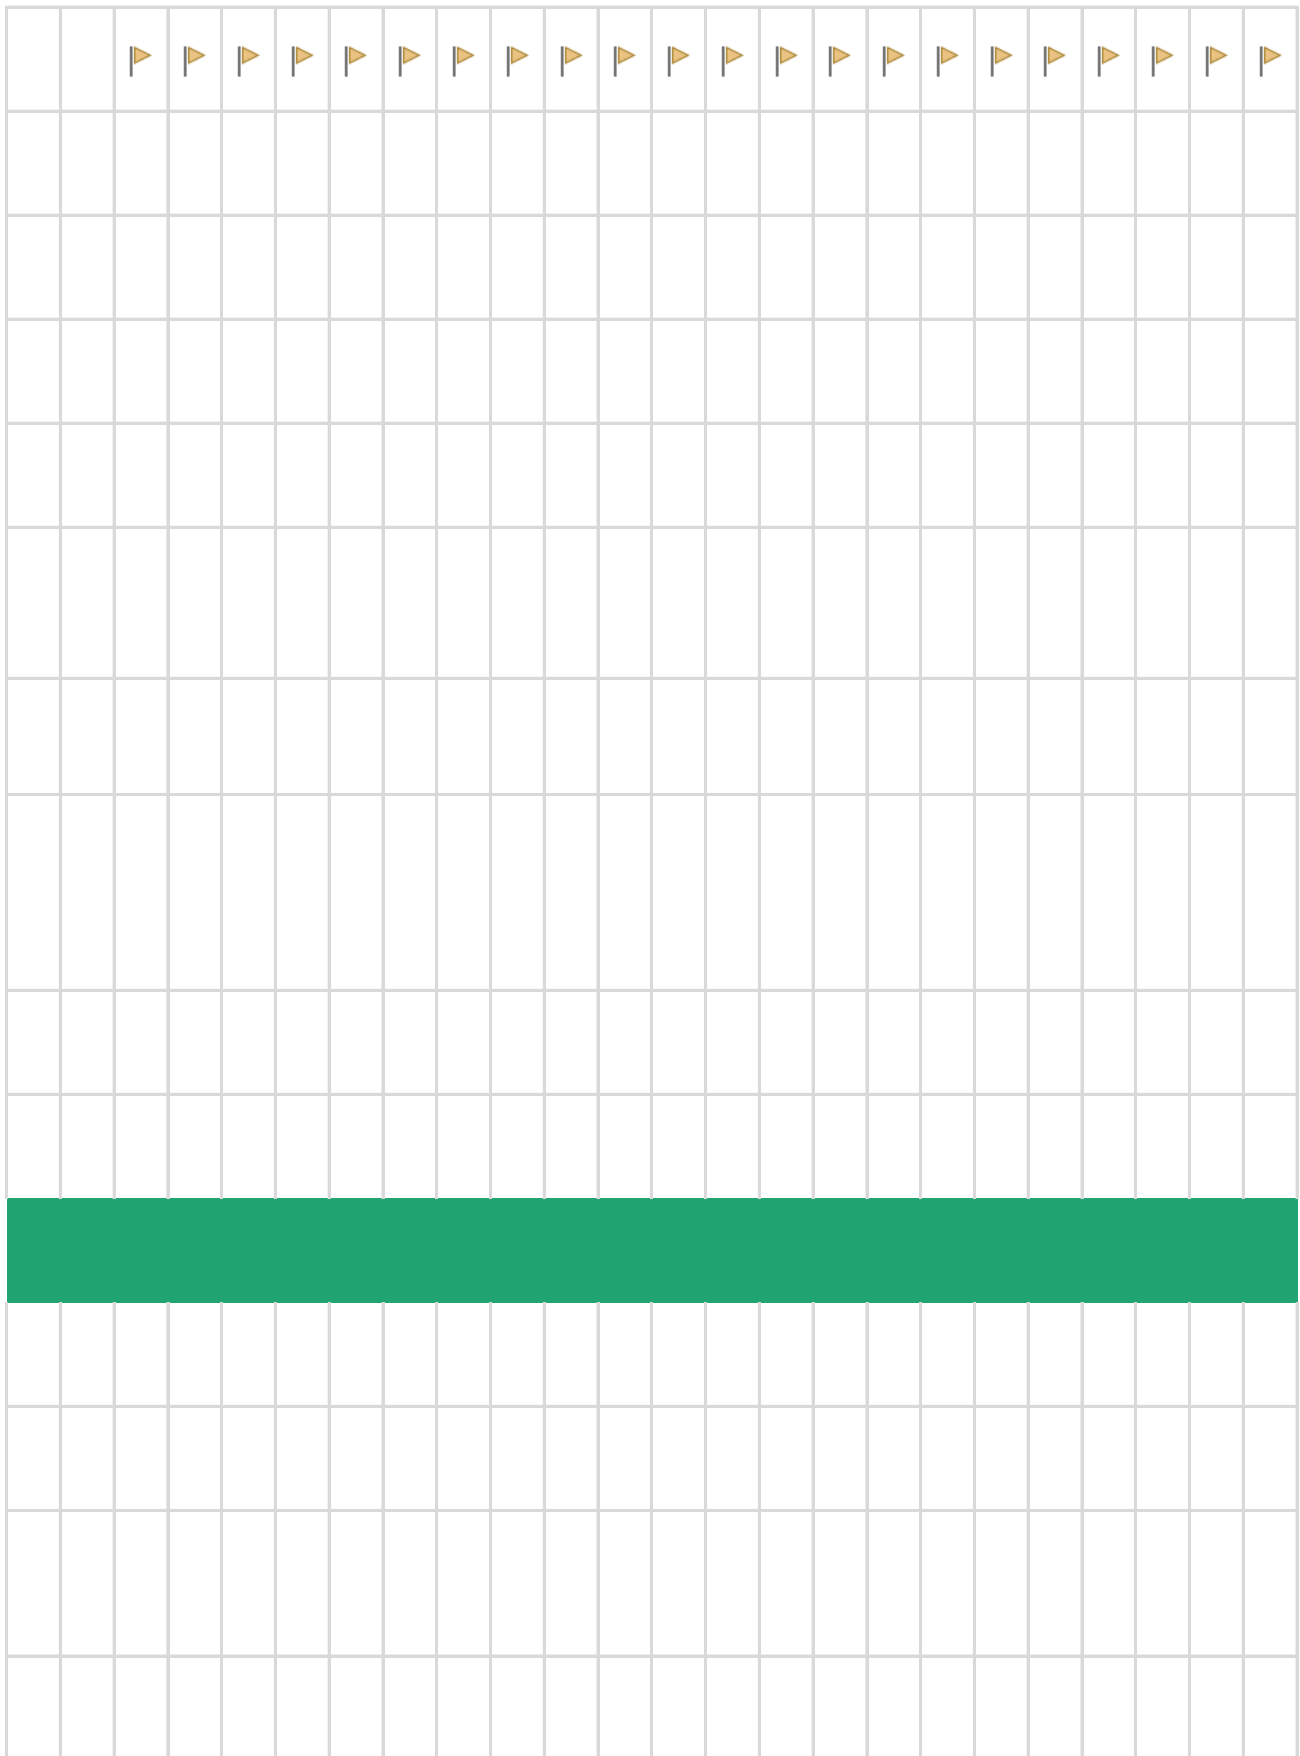

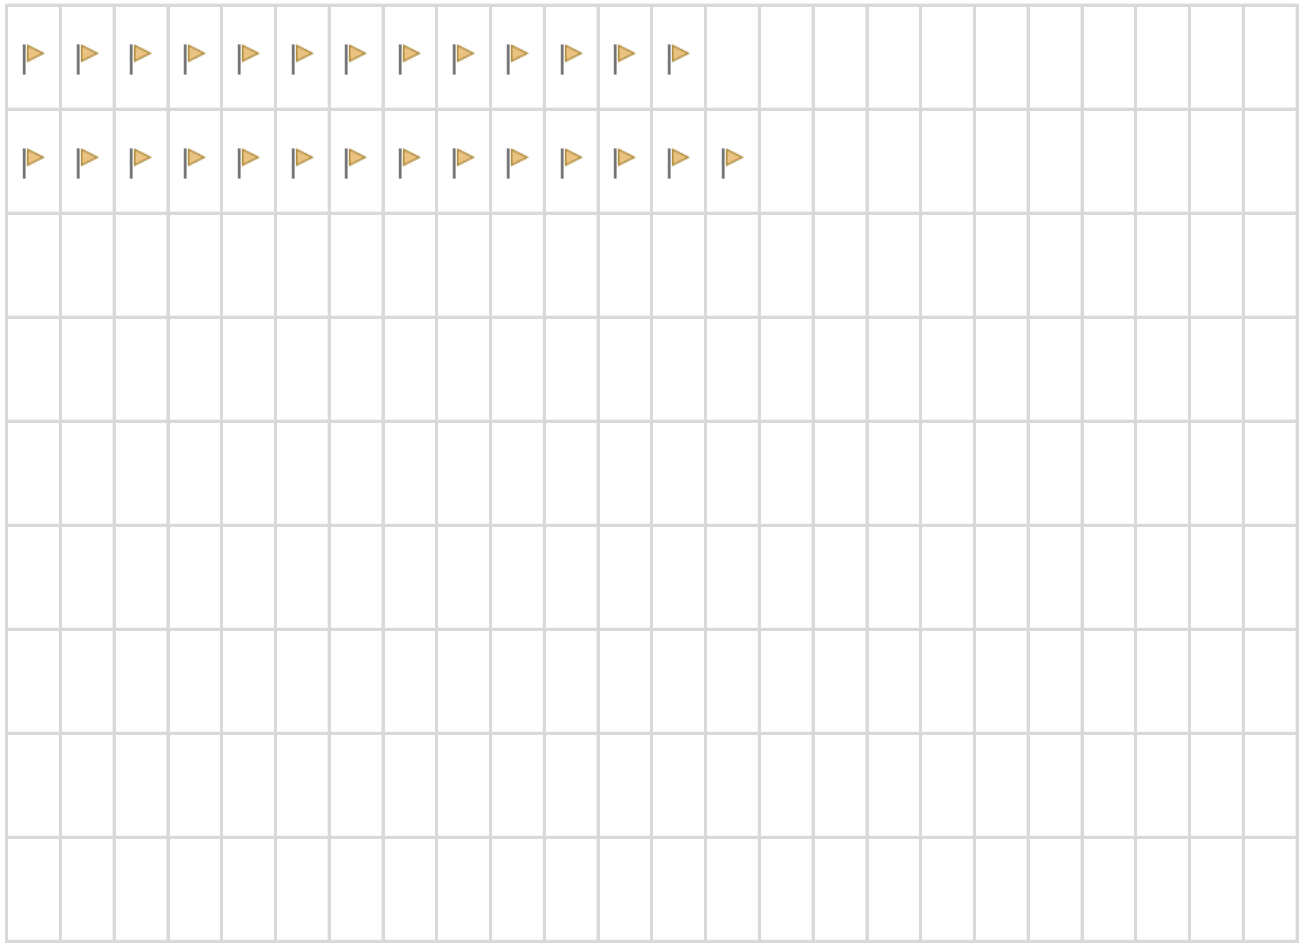



American Rescue Plan Act

City of Richmond

Building Back Greener and more Resilient

Project Start Date: 10/14/2021

Scrolling Increment: 5

Total Category

Total Category


Milestone description	Category	Assigned to
Climate Risk Assessment and Implementation		
Climate Vulnerability & Risk Assessment: Issue RFQ, identify consultant, create P.O.	Milestone	Alicia Zatcoff
Climate Vulnerability & Risk Assessment: Weekly meetings with consultant to create draft report	On Track	Alicia Zatcoff
Climate Vulnerability & Risk Assessment: Finalize report for inclusion in RVAgreen 2050: Climate Equity Action Plan 2030	Goal	Alicia Zatcoff
Urban Forest Master Plan: Draft scopes of work, create and execute work plan	On Track	Alicia Zatcoff
DPW Hire Urban Forester	On Track	Torrence Robinson
Urban Forest Master Plan: Establish Project Team	On Track	Alicia Zatcoff
Draft and issue RFQ for Assessment	Milestone	Alicia Zatcoff


Select Contractor for Assessment	Milestone	Alicia Zatcoff
Develop draft assessemnt	Milestone	Alicia Zatcoff
Final Assessment and close out	Goal	Alicia Zatcoff
Draft and issue RFP for Implementation	Milestone	Alicia Zatcoff
Select Contractor for Implementation	Milestone	Alicia Zatcoff
Final Plan	Milestone	Alicia Zatcoff
Planing Commission and City Council adoption	Milestone	Alicia Zatcoff
Plant Trees and Project Close out	Goal	Alicia Zatcoff
Lead Line Replacement Public Utilities		
Develop LSL Inventory Methodology	On Track	Jonathan Cosby
BlueConduit Donation of Data Services - Interactive Map	Low Risk	Jonathan Cosby
Conduct Inventory	On Track	Jonathan Cosby
Develop LSL Public Outreach and Education Programs	On Track	Jonathan Cosby
Conduct LSL Replacements (on-going)	On Track	Jonathan Cosby
Submit LSL Replacement Plan to VDH (as required by Lead & Copper Rule Revision)	Milestone	Jonathan Cosby
Stormwater		
Design	On Track	Bill Boston

Permitting	Milestone	Bill Boston
Property/ROW Acquisition	Med Risk	Bill Boston
Utility Relocations	Med Risk	Bill Boston
Contract Award	Milestone	Bill Boston
Construction	Goal	Public Utilities
Healthy Homes (Weatherization, Home Rehabilitation)		
Acquire a Construction Specialist/Rehab Inspector	On Track	Sherrill Hampton
Secure an Intake Specialist	On Track	Sherrill Hampton
Develop Program SOPs/Marketing Materials/General Housing Rehabilitation Specifications	On Track	Sherrill Hampton
Hold Interest Meetings for Community Outreach	Milestone	Sherrill Hampton
Receiving applications, ratings, and rankings for selction	Milestone	Sherrill Hampton


	0%	5/1/2023	30	5/31/2023						
	0%	6/1/2023	210	12/28/2023						
	0%	1/1/2024	30	1/31/2024						
	0%	2/1/2024	180	7/30/2024						
	0%	8/1/2024	90	10/30/2024						
	0%	11/1/2025	60	12/31/2025						
	0%	1/1/2026	180	6/30/2026						
	0%	9/1/2026	30	10/1/2026						
	20%	1/1/2022	350	12/17/2022						
	20%	6/1/2022	200	12/18/2022						
	10%	3/18/2022	750	4/6/2024						
	10%	3/18/2022	750	4/6/2024						
	0%	6/15/2022	1,650	12/21/2026						
	20%	1/1/2022	985	9/12/2024						
	100%	7/1/2020	730	7/1/2022						


100%	9/1/2021	180	2/28/2022						
100%	5/1/2021	380	5/16/2022						
50%	7/1/2022	274	4/1/2023						
5%	9/1/2022	180	2/28/2023	▶	▶	▶	▶	▶	▶
0%	6/1/2023	365	5/31/2024						
100%	3/1/2022	120	6/29/2022						
100%	3/1/2022	120	6/29/2022						
80%	5/1/2022	152	9/30/2022						
0%	7/1/2022	122	10/31/2022						
0%	8/15/2022	75	10/29/2022						

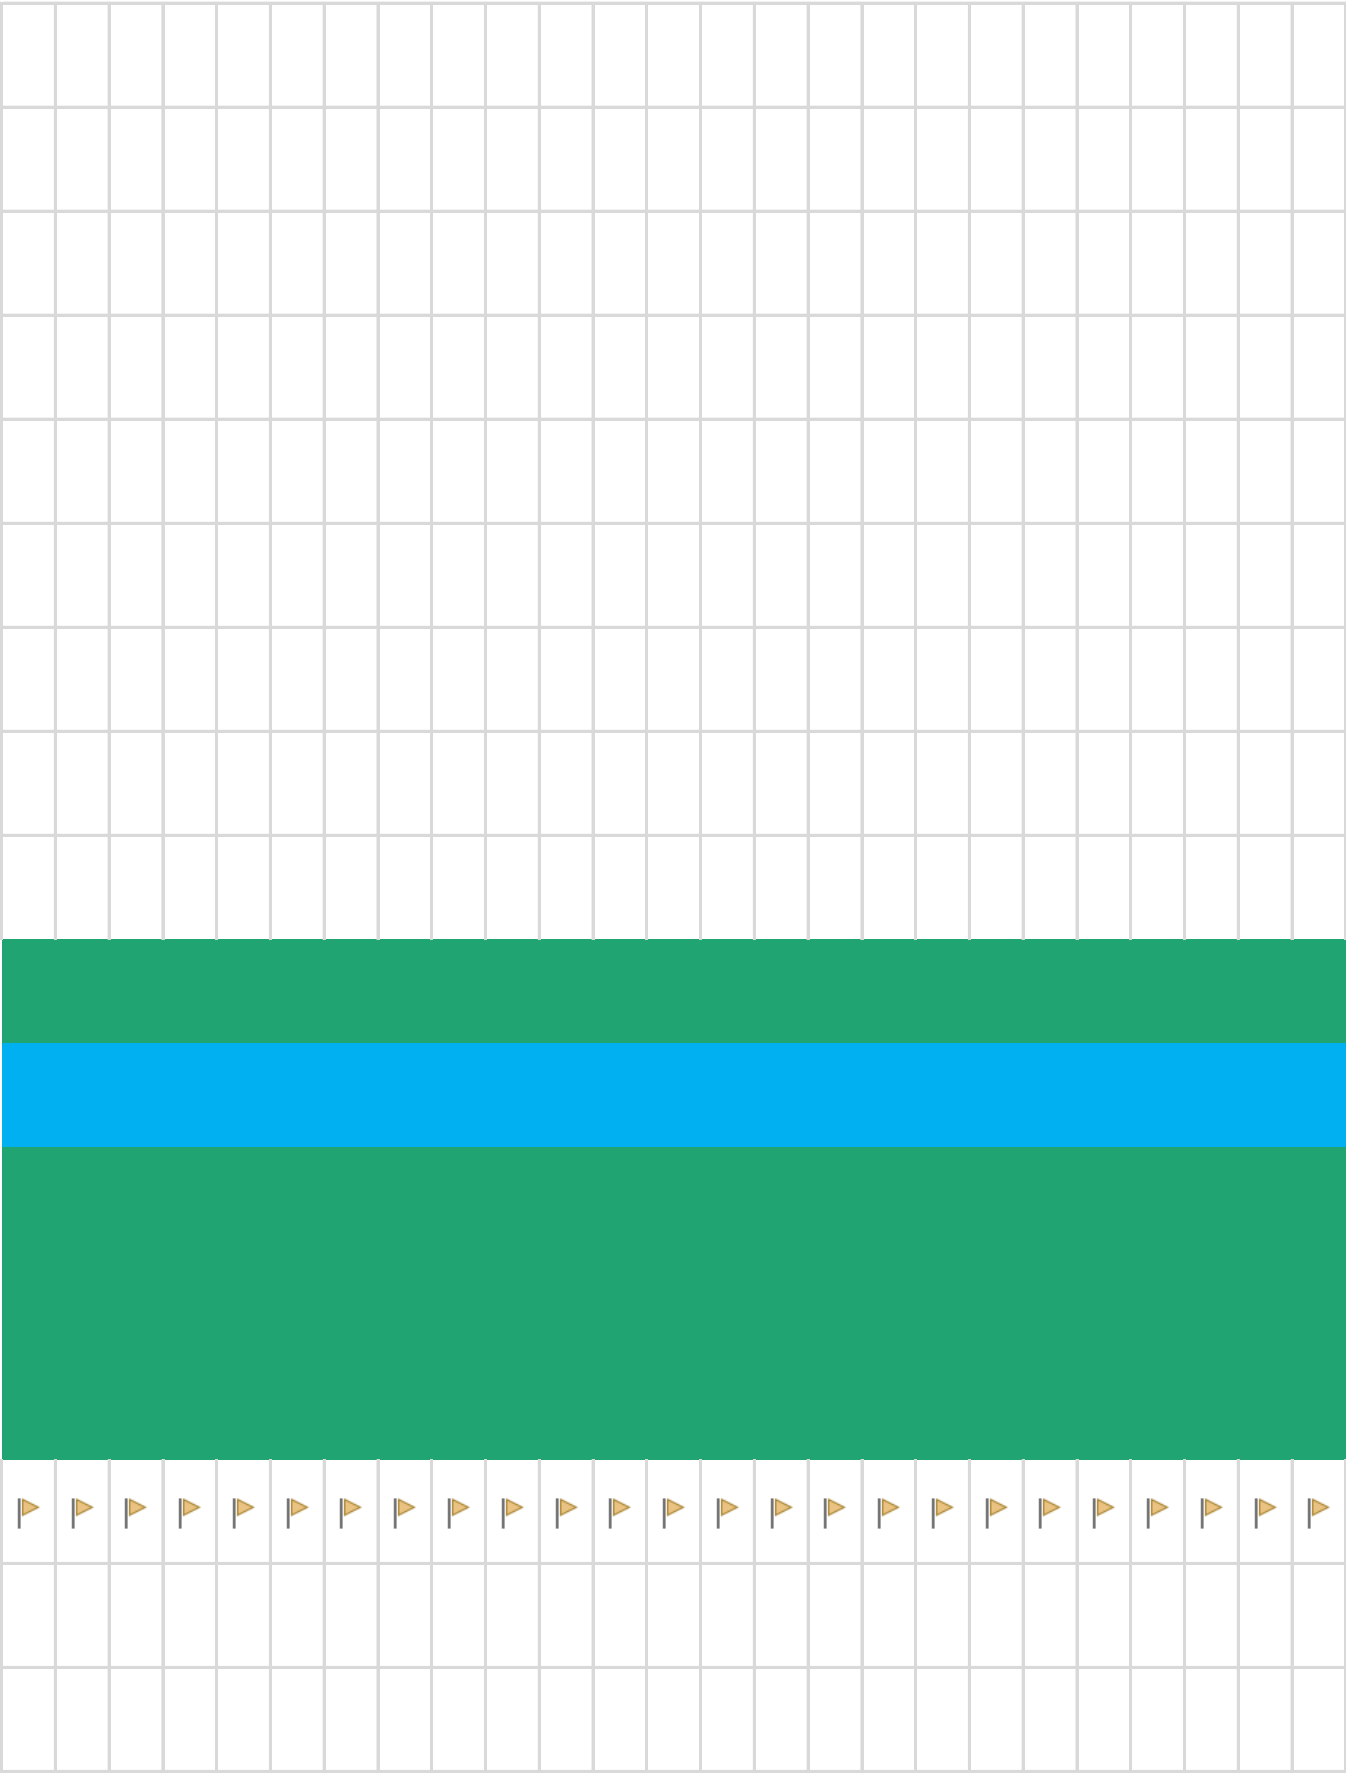

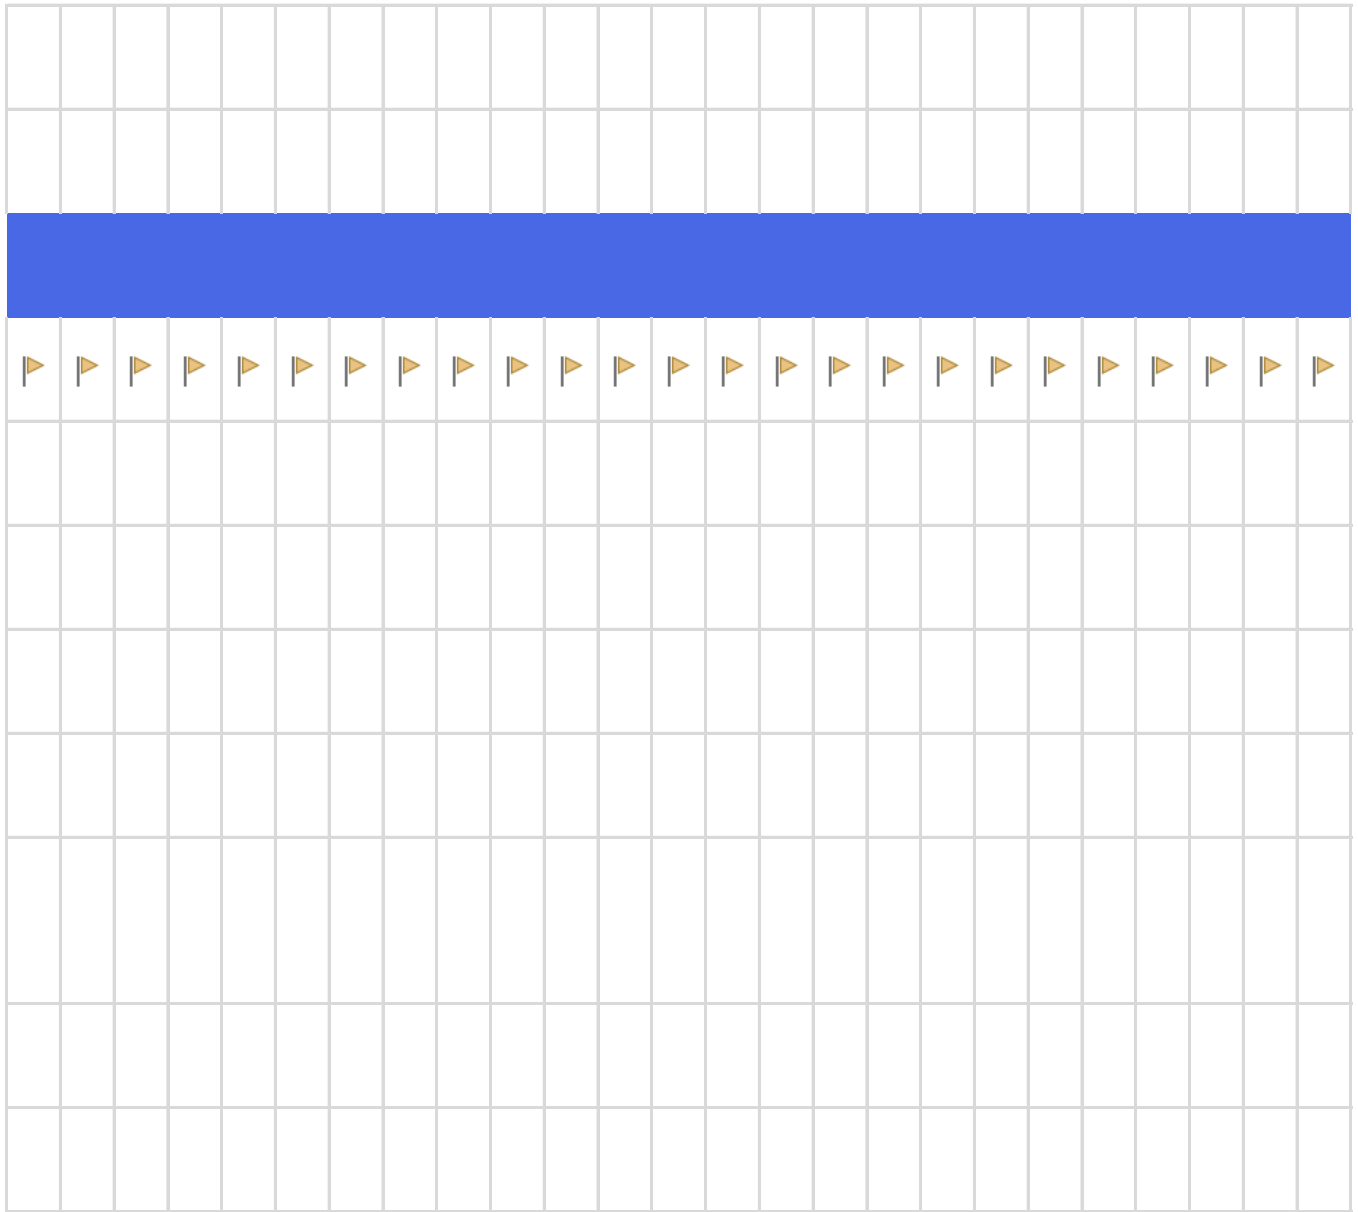

[illegible]

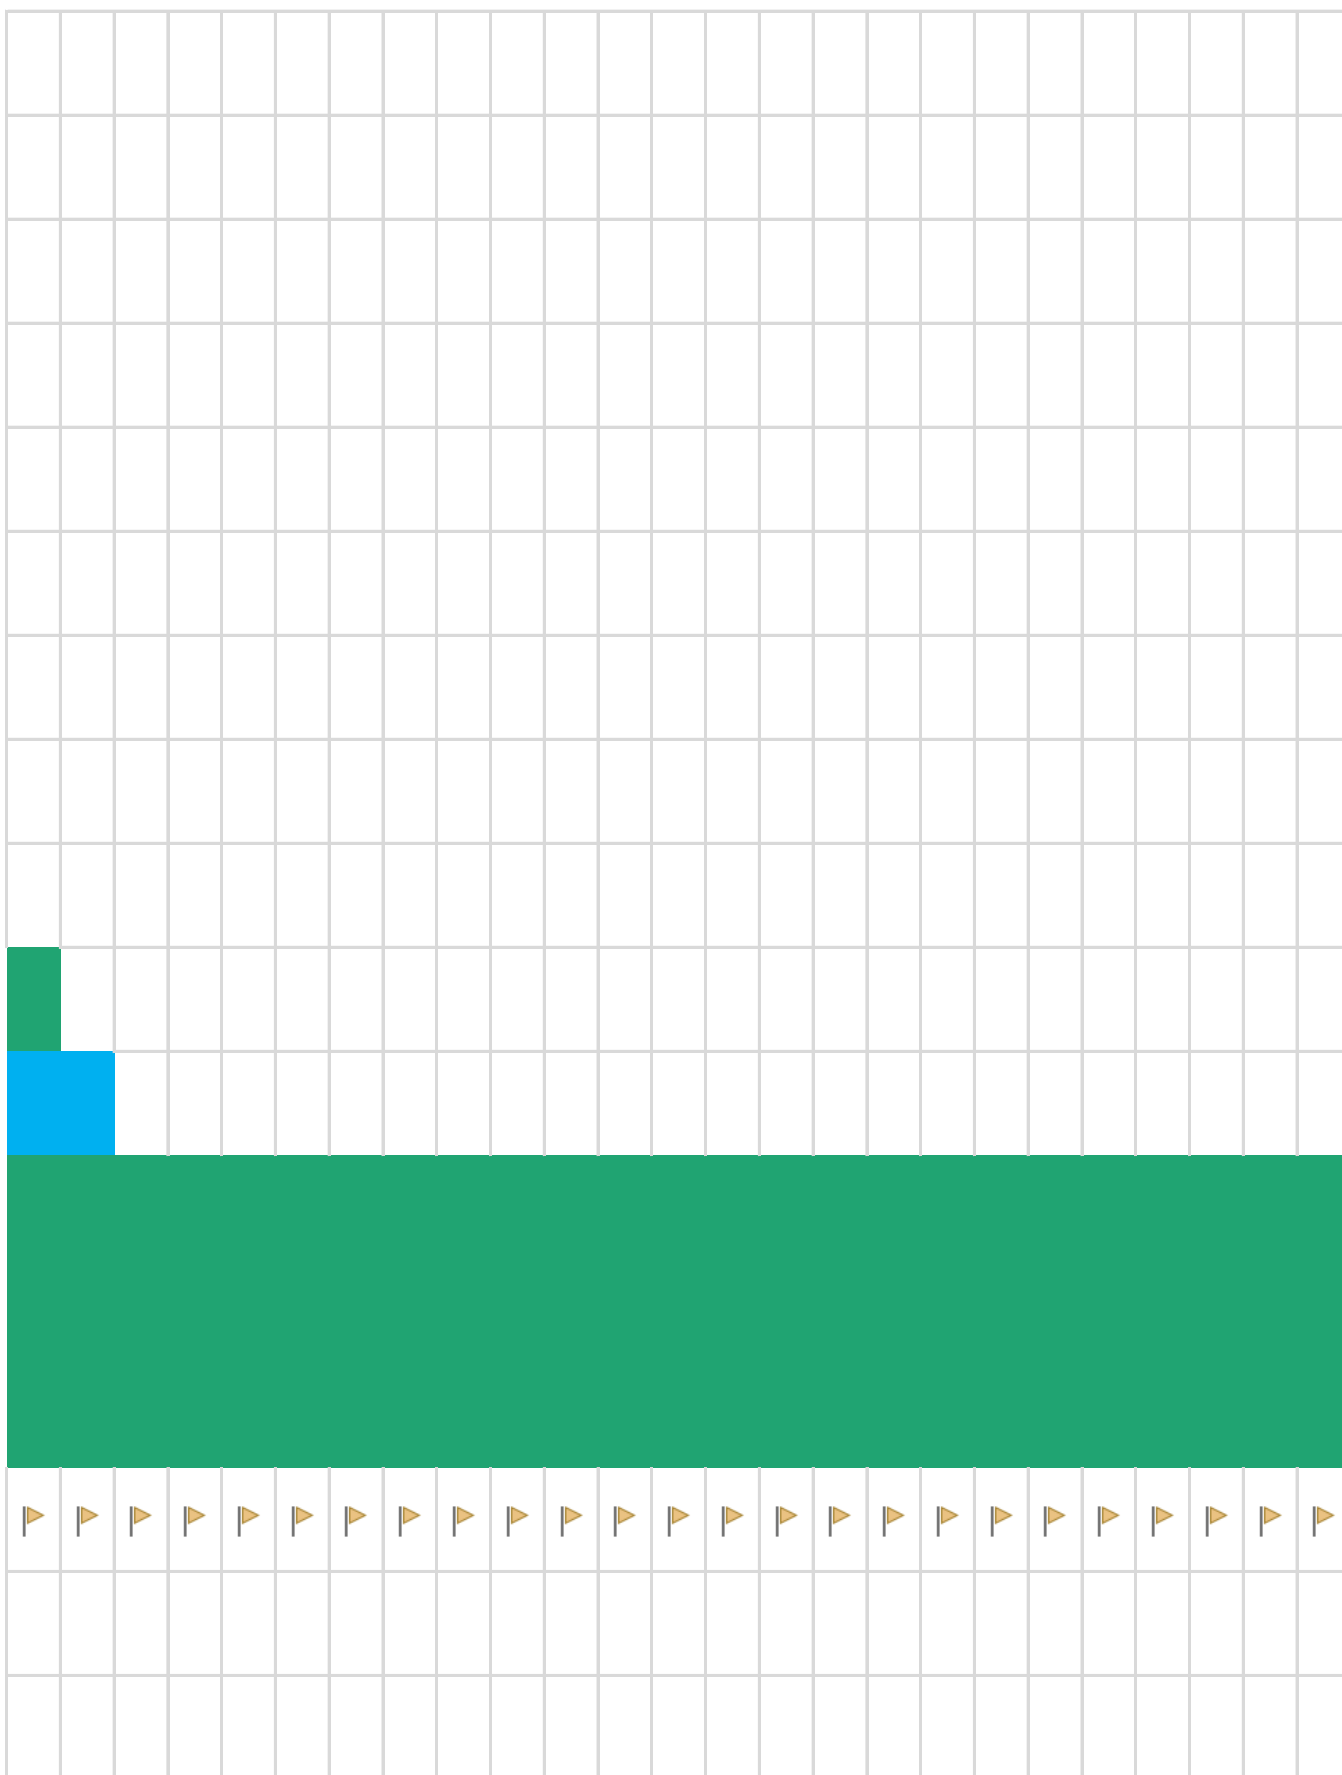

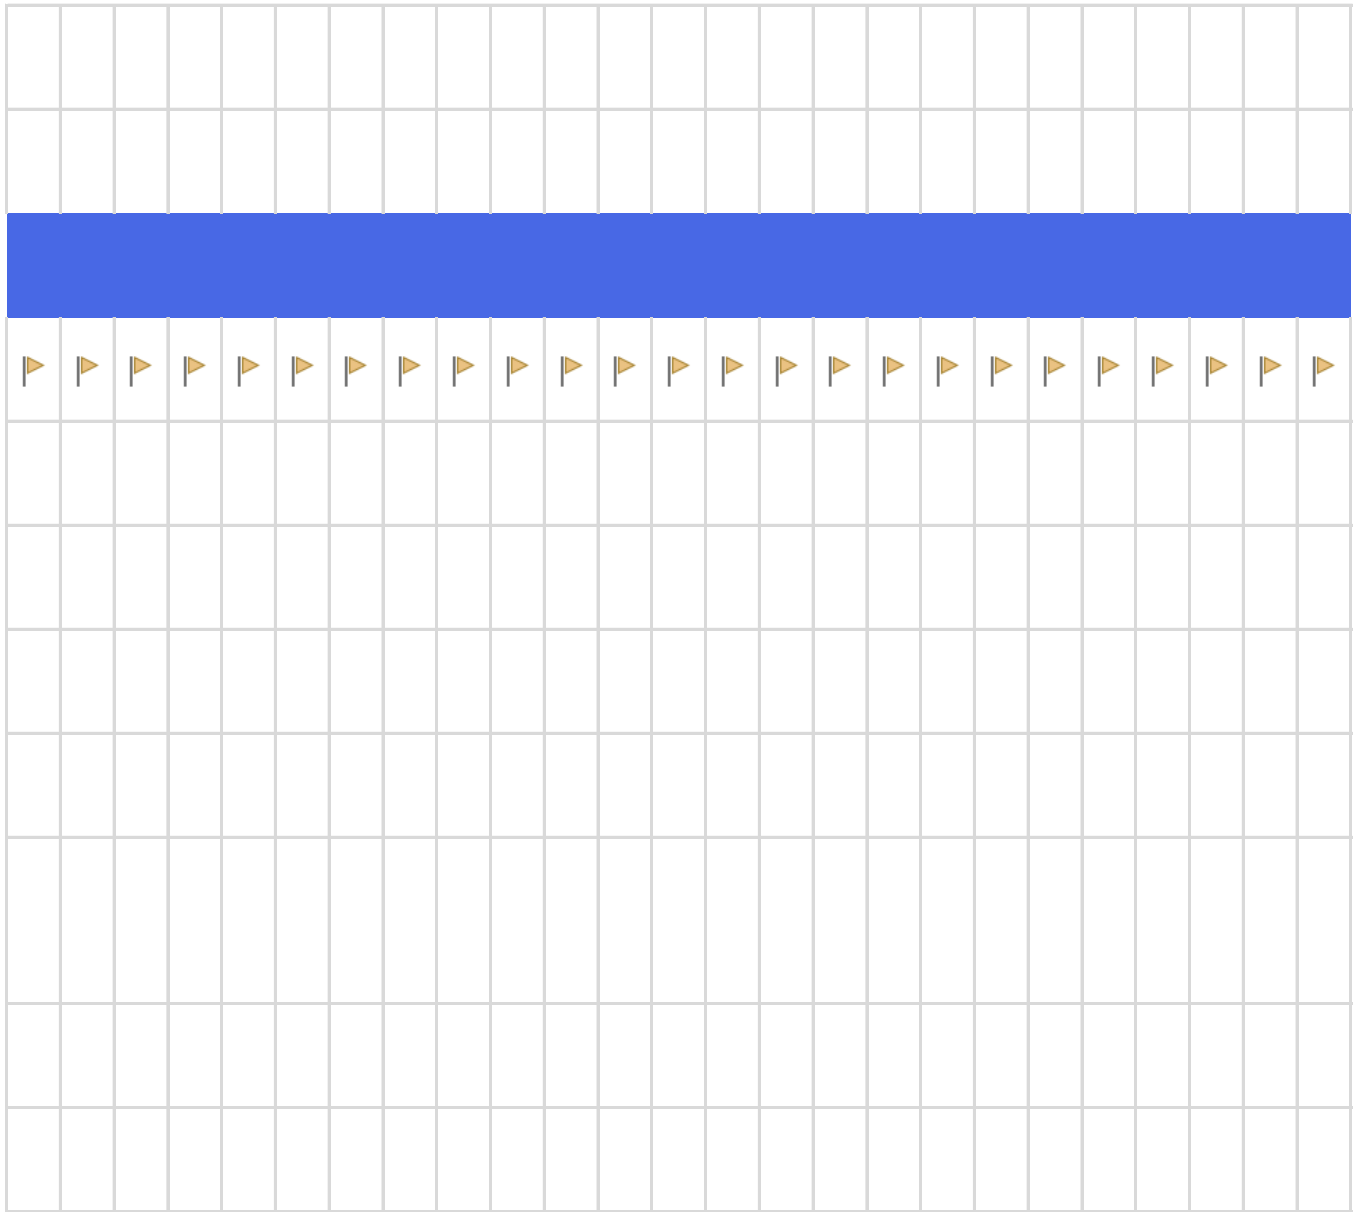



American Rescue Plan Act

City of Richmond

Building Back Safer

Project Start Date: 10/14/2021

Scrolling Increment: 96

Total Category A

Total Category Ex

Milestone description	Category	Assigned to
Gun violence prevention		
Identification/Announcement of Positive Youth Development/Youth Violence	Milestone	Eva Colen
MOU Executed with Fund Partner	Milestone	Eva Colen
Summer Programming RFP is Posted	Goal	Eva Colen
Summer Programming Begins	Goal	Eva Colen
Academic Year Programming RFP is posted	Goal	Eva Colen
Academic Year Programming Begins	Goal	Eva Colen
Scope and timeline of Gun Buyback program identified working with RPD and Community	Milestone	Maggie Anderson/ Megan Fields
Exploring potential third-party partners related to the Gun Buyback Program	Milestone	Maggie Anderson/ Megan Fields
Exploring best approach to Gun Safety PSA Campaign	On Track	Maggie Anderson/ Megan Fields

Gun Safety PSA Campaign Launch	Milestone	Maggie Anderson/ Megan Fields
Gun Buyback Program Launch (first Gun Buy Back event)	Milestone	Maggie Anderson/ Megan Fields
Planning for second Gun Buyback event	Goal	Maggie Anderson/ Megan Fields
Second Gun Buy Back event	Milestone	Maggie Anderson/ Megan Fields
First responders hazard pay		
Phase I - Public Safety Bonus for Public Safety	Milestone	Jason May/ Meghan Brown
Phase II - Public Safety Bonuses for RAA	Milestone	Jason May/ Meghan Brown
Enhanced Lighting (street and business) and cameras		
Request for quotes and project proposal	Goal	Jackie Crotts
IT Purchase Request	Goal	Jackie Crotts
Consultant Procurement for Deployment	On Track	Erich Bessey
Determine light and cameras	On Track	Erich Bessey

Legend:

On track

Low risk

Allocation (Tranche	7,500,000
penditure To-Date	6,155,202

Progress		Start	Days	End
				0
100%		1/1/2022	30	1/31/2022
100%		2/1/2022	90	5/2/2022
100%		4/30/2022	1	5/1/2022
100%		6/27/2022	1	6/28/2022
100%		8/1/2022	1	8/2/2022
100%		9/6/2022	1	9/7/2022
100%		2/1/2022	120	6/1/2022
100%		3/24/2022	60	5/23/2022
25%		3/28/2022	260	12/13/2022

[illegible]



High risk

Unassigned

[illegible]

